	Office	Duration	Start	Finish
1	**Resident Rep**	**10 days**	**Fri 07/02/20 08:00**	**Sun 16/02/20 17:00**
2	**Deputy Resident Rep**	**3 days**	**Fri 14/02/20 08:00**	**Sun 16/02/20 17:00**
3	**Program Associate**	**3 days**	**Fri 14/02/20 08:00**	**Sun 16/02/20 17:00**
4	**New Office 2- RCO**	**3 days**	**Fri 21/02/20 08:00**	**Sun 23/02/20 17:00**
5	**New Office 3 - RCO**	**3 days**	**Fri 21/02/20 08:00**	**Sun 23/02/20 17:00**
6	**Boardroom**	**17 days**	**Fri 14/02/20 08:00**	**Sun 01/03/20 17:00**
7	**New Office 4 - M&E**	**3 days**	**Fri 31/01/20 08:00**	**Sun 02/02/20 17:00**
8	**Main Meeting room**	**10 days**	**Fri 14/02/20 08:00**	**Sun 23/02/20 17:00**
9	**Former Reception**	**25 days**	**Fri 14/02/20 08:00**	**Mon 09/03/20 17:0**
10	**RC and RC Assistant**	**3 days**	**Fri 31/01/20 08:00**	**Sun 02/02/20 17:00**
11	**Open Plan Office**	**10 days**	**Fri 21/02/20 08:00**	**Sun 01/03/20 17:00**
12	**Second Floor Corrido**	**5 days**	**Fri 21/02/20 08:00**	**Tue 25/02/20 17:00**

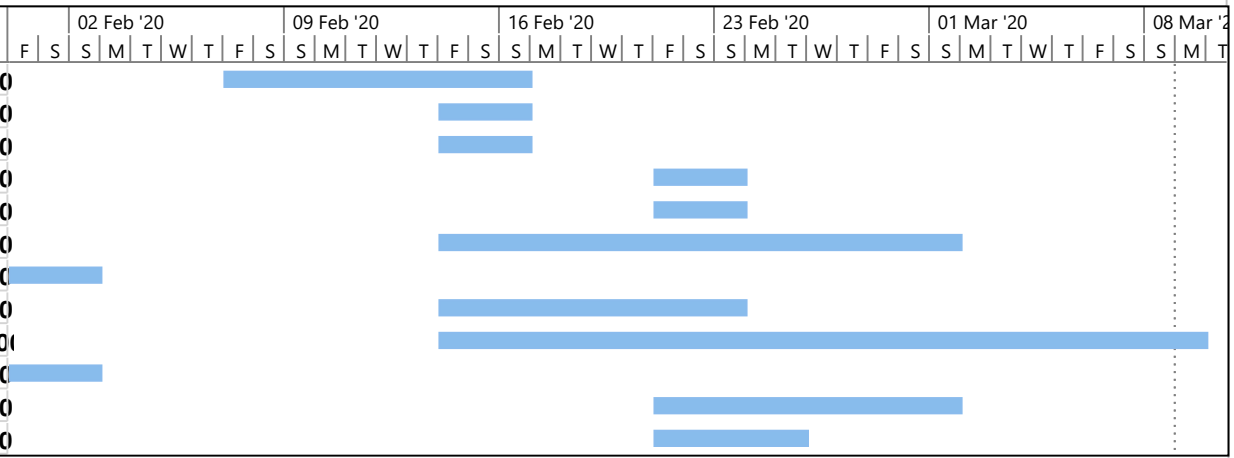

UNDP OFFICE
PARTITIONING AND
REFURBISHMENT

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
