



Empowered lives.  
Resilient nations.

REQUEST FOR QUOTATION (RFQ)  
(Civil Works )

<i>NAME &amp; ADDRESS OF FIRM</i>	DATE: May 18, 2018
	REFERENCE: Expansion and Improved Management Effectiveness of the Achara Region's Protected Areas, № 00088000

Dear Sir / Madam:

We kindly request you to submit your Quotation for **Rehabilitation of Machakhela National Park Administration and Visitor Centre Front Yard** as detailed in Annex I (Technical Specifications) and Annex II (Bill of Quantities) of this RFQ.

When preparing your quotation, please be guided by the form attached hereto as Annex II.

Signed and stamped quotations may be submitted on or before 18:00 hrs Georgia Standard Time (GMT+4), Friday, June 01, 2018 via email to the address below:

[Irakli.goradze@undp.org](mailto:Irakli.goradze@undp.org)

CC: [guranda.kartvelishvili@undp.org](mailto:guranda.kartvelishvili@undp.org)

*Contact Person: Irakli Goradze, Project Manager*

Your Proposal must be expressed in the English, and valid for a minimum period of 60 calendar Days.

In the course of preparing your Proposal, it shall remain your responsibility to ensure that it reaches the address above on or before the deadline. Proposals that are received by UNDP after the deadline indicated above, for whatever reason, shall not be considered for evaluation. Kindly ensure that required documents are signed, stamped and in the .pdf format (please also provide the BoQ in Excel Format), free from any virus or corrupted files, and max. file size per transmission 5 MB.

Please take note of the following requirements and conditions pertaining to the supply of the abovementioned civil works:

Exact Address of Delivery Location	Machakhela National Park Administration and Visitor Centre, Village Acharisagmarti, Khelvachauri municipality, Autonomous Republic of Achara, Georgia  <b>Note: Site visit is not envisaged within this RFQ, but bidders are strongly encouraged to visit the site on their own expenses.</b>
Latest Expected Delivery Date and Time	<input checked="" type="checkbox"/> No more than 2 months from the issuance of the Civil Works Contract
Delivery Schedule	<input checked="" type="checkbox"/> Required
Preferred Currency of Quotation	<input checked="" type="checkbox"/> Local Currency : <b>GEL (Georgian Lari)</b>  <b>For evaluation purposes bids submitted in other currency than UNDP preferred currency will be converted to GEL according to UN Official Rate of Exchange at the date of Bid Opening.</b>
Value Added Tax on Price Quotation	<input checked="" type="checkbox"/> Must be exclusive of VAT and other applicable indirect taxes
After-sales services required	<input checked="" type="checkbox"/> Warranty on works for the minimum period of one (1) year.  <b>Warranty details:</b> Warranty period starts from the date of substantial completion of works and it covers all construction and installation works. Any defects identified during the warranty period (1 year) will be assessed by expertize services and respectively identified responsible party shall be responsible for the compensation of loss.
A pre-bid conference will be held on:	Time: 15:00 hrs Georgia Standard Time (GMT+4) Date: 29 May 2018  The pre-bid conference will be held via Skype. Please contact the UNDP focal point for the arrangement: Guranda Kartvelishvili, Project Admin/Finance Assistant Email: guranda.kartvelishvili@undp.org Phone: +995 577 66 23 91
All documentations, shall be in this language	<input checked="" type="checkbox"/> <b>English - except for documents issued by Georgian State Agencies - Extract from Entrepreneurial Register and Detailed Bank Requisites.</b>
Documents to be submitted	<input checked="" type="checkbox"/> Duly Accomplished Form as provided in <b>Annex II</b> , and in accordance with the <b>Technical specification, Annex I</b> (All materials to be used for the rehabilitation shall comply with Technical Specification (Annex I). Brands and country of origins is required to be indicated. <b>Note: Please also provide the BoQ in Excel Format.</b> <input checked="" type="checkbox"/> <b>Company Profile:</b> General information (company name, address, contact person, profile, year established). <input checked="" type="checkbox"/> <b>An extract from the entrepreneurial register.</b> <input checked="" type="checkbox"/> CV's of the Key Employees – at least for the Civil Engineer.

	<p>The company is requested to nominate the person with whom UNDP will liaise within the period of the contract – Civil Engineer.</p> <p><input checked="" type="checkbox"/> Copies of Diploma of the Civil Engineer.</p> <p><input checked="" type="checkbox"/> <b>Valid quality certificates should be submitted by successful company</b> for the main materials to be used (Cement, Metal square pipe, Anticorrosive paint, Wood varnish) upon signature of contract, otherwise contract will not be granted.</p> <p><input checked="" type="checkbox"/> <b>Detailed Bank requisites.</b></p> <p><input checked="" type="checkbox"/> <b>Bank Statement/Letter on annual turnover on past two (2) years (2016,2017).</b></p> <p><input checked="" type="checkbox"/> Tax Registration/Payment Certificate issued by the Internal Revenue Authority evidencing that the Bidder is updated with its tax payment obligations – <b>no debts towards budget exist</b>, or Certificate of Tax exemption, if any such privilege is enjoyed by the Bidder.</p>
<p>Period of Validity of Quotes starting the Submission Date</p>	<p><input checked="" type="checkbox"/> <b>60 days</b></p> <p>In exceptional circumstances, UNDP may request the Vendor to extend the validity of the Quotation beyond what has been initially indicated in this RFQ. The Proposal shall then confirm the extension in writing, without any modification whatsoever on the Quotation.</p>
<p>Partial Quotes</p>	<p><input checked="" type="checkbox"/> Not permitted</p>
<p>Payment Terms</p>	<p><input checked="" type="checkbox"/> Payment will be made in 2 installments after successful completion of each stage of the works specified in the contract.</p> <p><b><u>No advance payment will be done for the contract.</u></b></p>
<p>Liquidated damages</p>	<p><input checked="" type="checkbox"/> The liquidated damages for delay shall be 1 % of the price of the Contract per week of delay, up to a maximum of 10% of the final price of the Contract.</p>

<p>Evaluation Criteria</p>	<p><input checked="" type="checkbox"/> <u>Organizational Capacity:</u></p> <ul style="list-style-type: none"> <li>• Minimum no. of similar projects undertaken over the past 3 (three) years: 2 (two);</li> <li>• Minimum number of employees with respective duties and responsibilities:</li> </ul> <p>In total at least eight (8) Employees:</p> <p><input checked="" type="checkbox"/> Chief Civil Engineer – 1 person - with minimum three years of relevant experience, relevant education in the field of Engineering;</p> <p>Minimum number of employees with respective duties and responsibilities:</p> <p><input checked="" type="checkbox"/> Foreman of Construction Site – 1 person;  <input checked="" type="checkbox"/> Welder – 1 person;  <input checked="" type="checkbox"/> Carpenter – 1 person;  <input checked="" type="checkbox"/> Concrete worker – 1 person;  <input checked="" type="checkbox"/> Assistant worker – 1 person.</p> <p><input checked="" type="checkbox"/> Financial Capacity:  At least USD 100,000.00 of annual turnover per year for the past two years (2016,2017).  No debts towards budget exist.</p> <p><input checked="" type="checkbox"/> Full acceptance of General Terms and Conditions.</p> <p><input checked="" type="checkbox"/> Technical responsiveness (Annex I)/Full compliance to requirements and lowest price.</p> <p>List and minimum (number and requirement) equipment and machinery to be used:  <input checked="" type="checkbox"/> Concrete-mixer 0.5 m<sup>3</sup> ( ბეტონმრევი 0,5 m<sup>3</sup>), Welding Equipment (შესადღებელი აპარატი სტაციონალური) , Soil Compactor (გრუნტის სატკეპნი), Diezelgenerator 7 kW (დიზელგენერატორი 7 კვტ)</p>
<p>UNDP will award to:</p>	<p><input checked="" type="checkbox"/> One and only one supplier</p>
<p>Type of Contract to be Signed</p>	<p><input checked="" type="checkbox"/> Contract for Works</p>
<p>Conditions for Release of Payment</p>	<p>UNDP shall effect payment of the invoices after receipt of the certificate of payment issued by the Engineer, approving the amount contained in the invoice. The Engineer may make corrections to that amount, in which case UNDP may effect payment for the amount so corrected. The Interim Acceptance Certificate is made upon completion of every stage of works. The Engineer may also withhold invoices if the work is not performed at any time in accordance with the terms of the Contract.</p>

Annexes to this RFQ	<input checked="" type="checkbox"/> Technical Specifications (Annex 1) <input checked="" type="checkbox"/> Form for Submission of Quotation (Annex 2) <input checked="" type="checkbox"/> General Terms and Conditions for Civil Works (Annex 3) <input checked="" type="checkbox"/> Drawing (Annex 4)  Non-acceptance of the terms of the General Terms and Conditions (GTC) shall be grounds for disqualification from this procurement process.
Contact Persons for Inquiries (Written inquiries only)	Irakli Kipiani- Engineer Tel: +995 599 53 25 09  Irakli Goradze - Project Manager Tel: +995 577 454882 E-Mail: <a href="mailto:irakli.goradze@undp.org">irakli.goradze@undp.org</a>  Note: Latest date for submitting Inquiries two days before the deadline, <b>30 May 2018</b>  Any delay in UNDP’s response shall not be used as a reason for extending the deadline for submission, unless UNDP determines that such an extension is necessary and communicates a new deadline to the Proposers.

Civil works offered shall be reviewed based on completeness and compliance of the quotation with the minimum specifications described above and any other annexes providing details of UNDP requirements.

The quotation that complies with all of the specifications, requirements and offers the lowest price, as well as all other evaluation criteria indicated, shall be selected. Any offer that does not meet the requirements shall be rejected.

Any discrepancy between the unit price and the total price (obtained by multiplying the unit price and quantity) shall be re-computed by UNDP. The unit price shall prevail and the total price shall be corrected. If the supplier does not accept the final price based on UNDP’s re-computation and correction of errors, its quotation will be rejected.

After UNDP has identified the lowest price offer, UNDP reserves the right to award the contract based only on the prices of the goods in the event that the transportation cost (freight and insurance) is found to be higher than UNDP’s own estimated cost if sourced from its own freight forwarder and insurance provider.

At any time during the validity of the quotation, no price variation due to escalation, inflation, fluctuation in exchange rates, or any other market factors shall be accepted by UNDP after it has received the quotation. At the time of award of Contract or Purchase Order, UNDP reserves the right to vary (increase or decrease) the quantity of services and/or goods, by up to a maximum twenty five per cent (25%) of the total offer, without any change in the unit price or other terms and conditions.

Any Purchase Order that will be issued as a result of this RFQ shall be subject to the General Terms and Conditions attached hereto. The mere act of submission of a quotation implies that the vendor accepts without question the General Terms and Conditions of UNDP herein attached as Annex 3.

UNDP is not bound to accept any quotation, nor award a contract/Purchase Order, nor be responsible for any costs associated with a Supplier's preparation and submission of a quotation, regardless of the outcome or the manner of conducting the selection process.

Please be advised that UNDP's vendor protest procedure is intended to afford an opportunity to appeal for persons or firms not awarded a purchase order or contract in a competitive procurement process. **In the event that** you believe you have not been fairly treated, you can find detailed information about vendor protest procedures in the following link:

<http://www.undp.org/content/undp/en/home/operations/procurement/protestandsanctions/>

**UNDP encourages every prospective Vendor to** avoid and prevent conflicts of interest, by disclosing to UNDP if you, or any of your affiliates or personnel, were involved in the preparation of the requirements, design, specifications, cost estimates, and other information used in this RFQ.

UNDP implements a zero tolerance on fraud and other proscribed practices, and is committed to identifying and addressing all such acts and practices against UNDP, as well as third parties involved in UNDP activities. UNDP expects its suppliers to adhere to the UN Supplier Code of Conduct found in this link : [http://www.un.org/depts/ptd/pdf/conduct\\_english.pdf](http://www.un.org/depts/ptd/pdf/conduct_english.pdf)

**Thank you and we look forward to receiving your quotation.**

Sincerely yours,



Irakli Goradze  
Project Manager  
Project: Expansion and Improved Management Effectiveness  
of the Achara Region's Protected Areas

Annex I

## Technical Specifications

### Explanatory Note


Construction and repair works will be carried out in Machakhela National Park Administration Building and Visitor Centre, Village Acharisagmarti, Khelvachauri municipality, Autonomous Republic of Abkhazeti, Georgia. The building of the administration center was fully rehabilitated, and at this stage is planned rehabilitation of the yard. The picture shows the current situation of the object.



1




2

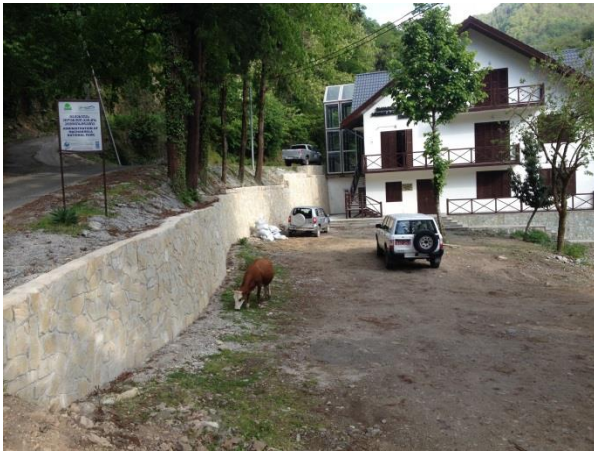

3



4

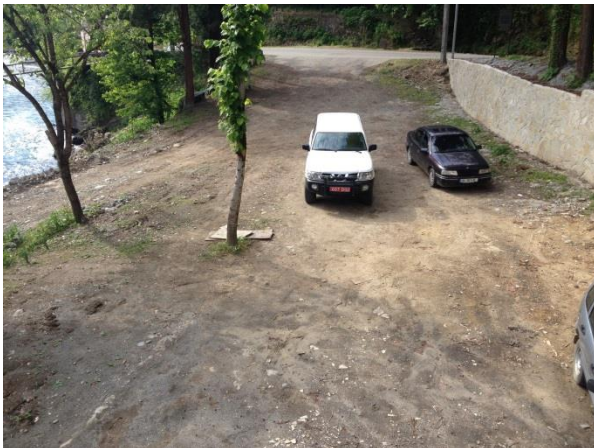

5



6

Projecting area is in Khelvachauri Municipality. The area includes the cadastral unit (22.33.02.025) with an area of 960 m<sup>2</sup> size. The terrain of the project area is inclinational surface.

Project Plant area - 265.38m<sup>2</sup>.

Rehabilitated building is a two-storey building with basement and a mansard. The building has two entrances. One is from the yard and another is from motorway side on the second floor level. At this stage the following main works have to be performed:

1. Arrangement of monolithic concrete wall, thickness 30 cm, length 31 m
2. Installation of fence and gates with metal square pipes, height of 100 cm, total length of 58 m
3. Ground transportation by truck, pavement and compacting
4. Arrangement of grass cover (rolling lawn) 170 m<sup>2</sup>
5. Laying with artificial concrete tiles 32.5 m<sup>2</sup>
6. Installation a bicycle parking at 10 bicycles
7. Blackout the fiberglass walls and roof with dark tone membrane 62 m<sup>2</sup>
8. Installation of a square benches (3 pc) and square urn,( 3 pc)
9. Arrangement banner with bilingual inscription and logo



7. Bicycle parking



8. Urn. Design/color to be agreed with client





9. square metal benches. Design/color to be agreed with client



10. inscription on the facade



11. Banner

Inscription: მაჭახელას ეროვნული პარკი /Machakhela National Park



12. Logo

**The basic requirements of the construction works:**

During performing construction-installation works strictly should be considered the safety technic requirements as well as fire prevention measures. The dangerous zones during performing works should be outlined and warning signs and writing should be present at the line borders.

The work of construction mechanisms is prohibited under the electricity transmitting lines.

The working personal should be instructed about the construction-installation work safety and fire prevention activities.

The fire prevention means should be provided to the work site.

The material storage should be performed according to technological requirements.

For performing any kind of construction, installation and transportation tasks, the safety technic requirements should be employed – SNIP III –4-80 “Safety Technic in Construction”.

**1. Cement**

Portland cement, grade M-400 EN 197-1. Cement shall be ordinary Portland cement type and sulphate resistant in accordance with state standards ГOCT (GOST) 22266-76 (ASTM C150 or B.S 12) unless otherwise instructed. The make and quality of cement to be used in the work shall be subject to the approval of the UNDP Engineer

**2. Sand-Cement mortar**

For improved plastering of façade and inner wall : grade M-50; Mix ingredients: sand – quartz, cement – Portland M-400 For sand-cement underlayment – mix - normal, 1:3, fraction of washed sand – 2mm;

**3. Gravel, Sand**

The gravel should be in conformity with broken material taken from the river, the washed fraction indicated in the drawings. The each pebble should have all sides broken. Weight by volume must be 1800 – 1900 kg/m<sup>3</sup>.

Sand for filling shall be non-saline and consist of hard, dense and durable materials, and shall be free from of clay-lumps, light weight material, or other deleterious substances. They shall to comply fully with the requirements as laid down for fine aggregates

**4. Metal**

Metal square pipes must meet the standards and additional Euronorm 19-57 DIN 1025 Euronorm 19-57 (Dimensions ), EN 10034: 1993 (Tolerances ) and EN 10163-3, C (surface quality), metal sheet made in accordance with the standards ГOCT 103-76.

Making and processing with anticorrosive paint every metal elements. Welding with electrode E-42

**5. Armature**

Reinforcement for reinforcement concrete structure: periodic Ø-16AIII Ø-12AIII, for maximum extreme tension load 3400kgf/cm<sup>2</sup>, for a clip band - Ø-8AI, for maximum extreme tension load 2100kgf/cm<sup>2</sup>. Reinforcement of AI and AIII class used in the project should correspond to ГOCT 5781-82

**6. Rolling Lawn**

The lawn age should be at least 2 years without cutting, cutting height of 4-5 cm, cutting width 45-50 cm. The grass rods are approximately 50 pounds at 10 cm. It must have a well-developed root system.

## **7. Wooden materials**

Materials used for Banner should be of coniferous tree, coefficient of humidity should be no more than 20% (humidity of the wood at the construction site will be measured with a special tool). The wood should be free of boughs – no more than 10% of total area, should be clean of bark.

Wooden materials should be processed with Antibacterial and fire prevention solution.

## **8. Anticorrosion Paint**

Acrylic oil wear-proof paint of high quality and anticorrosion effect – two layers, UV emanation steadiness (class of resistance to wear EN 13300 Class).

## **9. Antiseptic**

Antiseptic should protect the wooden material from atmospheric influence, rot mushrooms, fungi. Should insure long-term protection from biodamage.

## **10. Varnish**

Varnish should be of outdoor usage, should provide steam carrying, water resistance, resistance from mechanic influence, wear-out resistance, and UV emanation steadiness.

## **Quality Control during Contract Implementation**

The Contractor shall be responsible for the quality of the works for the entire construction work within the Contract. He shall, therefore, have his own independent and adequate set-up for ensuring the same.

Before the commencement of works, the contractor and UNDP engineer agree upon the quality assurance methods of construction-installation works according to the existing construction norms and requirements.

Construction materials, items and equipment should meet international standards and ecology requirements and should have appropriate certificate.

Construction norms and regulations (SNiP-III-18-75 and SNiP-III-4-80) requirements should be followed. Safety rules should be strictly observed.

Construction materials, tools and equipment should be correspondent to international standards, should meet ecology requirements and should have corresponding certificate.

**Colors of the materials to be used should be agreed with the costumer and technical supervisor of the renovation project.**

## **განმარტებითი ბარათი**

სამშენებლო-სარემონტო სამუშაოები ჩატარდება მაჭახელას ეროვნული პარკის ადმინისტრაციის და ვიზიტორთა ცენტრის შენობის მიმდებარე ტერიტორიაზე, სოფ. აჭარისაღმართში ხელვაჩაურის მუნიციპალიტეტში.

ადმინისტრაციის ცენტრის შენობას ჩაუტარდა სრული რეაბილიტაცია, და ამ ეტაპზე იგეგმება შენობის ეზოს კეთილმოწყობა. სურათებზე მოცემულია ობიექტის ახლანდელი მდგომარეობა.

სარეაბილიტაციო ობიექტი მდებარეობს ხელვაჩაურის მუნიციპალიტეტში. ტერიტორია მოიცავს საკადასტრო ერთეულს (22.33.02.025) რომლის ფართი 960 მ2 ია. ტერიტორიის რელიეფი ქანობიანი ზედაპირითაა წადგენილი. საპროექტო განაშენიანების ფართი - 265 ,38მ2; რეაბილიტირებული შენობა წარმოადგენს ორ სართულიან ნაგებობას სარდაფით და მანსარდით. შენობას აქვს ორი შესასვლელი,-ერთი ეზოს მხრიდან და მეორე საავტომობილო გზის მხრიდან მეორე სართულის დონეზე, სადაც მოწყობილია შემინული კიბის უჯრედი.

ამ ეტაპზე ჩასატარებელია შემდეგი ძირითადი სამუშაოები:

1. რკინაბეტონის კედლის მოწყობა სისქით 30 სმ, სიგრძით 31 მ.
2. ლითონის ღობის მოწყობა მილკვადრატებით სიმაღლით 100 სმ, საერთო სიგრძით 58 მ.
3. ტერიტორიაზე გრუნტის შემოტანა და მოსწორება.
4. რულონური გაზონის მოწყობა 170 მ2.
5. ბეტონის ფილაქანის მოწყობა 32,5 მ2.
6. ველოპარკინგის მოწყობა 10 ველოსიპედზე.
7. შემინული კიბის უჯრედის დაბურვა ტონირებული ფირით 62 მ2.
8. სკვერის სკამის (3 ცალი) და ურნის (3 ცალი) მონტაჟი.
9. სარეკლამო ბანერის მოწყობა ორენოვანი წარწერით და სააგენტოს ლოგოს დატანით.

#### **ძირითადი მოთხოვნები სამშენებლო სამუშაოების მიმართ:**

სამშენებლო-სამონტაჟო სამუშაოების შესრულების დროს მკაცრად უნდა იყოს დაცული უსაფრთხოების ტექნიკის მოთხოვნები, აგრეთვე უნდა გატარდეს ხანძარსაწინააღმდეგო ღონისძიებები.

სახიფათო ზონები სამუშაოების შესრულებისას უნდა მოინიშნოს გამაფრთხილებელი ნიშნებით. სამშენებლო მექანიზმების მუშაობა აკრძალულია შესაბამის ორგანოებთან, სპეციალური შეთანხმების გარეშე, ელექტროგადამცემ ხაზებთან და სხვა კომუნიკაციებთან ახლოს.

ყოველი მუშა პირადად უნდა იყოს ინფორმირებული სამშენებლო-სამონტაჟო სამუშაოების უსაფრთხოებისა და ხანძარსაწინააღმდეგო საქმიანობის შესახებ.

სამუშაო არეალი უნდა იყოს აღჭურვილი ხანძარსაწინააღმდეგო საშუალებებით.

მასალის შენახვის პირობები უნდა აკმაყოფილებდეს ტექნოლოგიურ მოთხოვნებს.

ნებისმიერი სახის სამშენებლო, სამონტაჟო სამუშაოების შესრულების და ტრანსპორტირების დროს, უნდა იყოს დაცული უსაფრთხოების ტექნიკის მოთხოვნები- snip III -4-80 "უსაფრთხოების ტექნიკა მშენებლობა"-ის მიხედვით.

#### **1. ცემენტი**

პორტლანდცემენტი, მარკა M-400 (EN 197-1) ცემენტი უნდა იყოს სულფატების მიმართ მდგრადი, და უნდა შეესაბამებოდეს სახელმწიფო სტანდარტებს GOCT (GOST) 22266-76 (ASTM C150 ან B.S 12) ცემენტის მარკა და ხარისხი გამოყენებამდე უნდა იყოს შეთანხმებული UNDP ინჟინერთან

#### **2. ქვიშა-ცემენტის ხსნარი**

გაუმჯობესებული შელესვა ფასადის და შიდა კედლის და იატაკის მოჭიმვა. მარკა M-50; შემავსებლები: ქვიშის - კვარცი, ცემენტი - მარკა M-400 ქვიშა-ცემენტის შეფარდება- ნორმალური, 1: 3, გარეცხილი ქვიშა - 2 მმ;

### 3. ხრეში, ქვიშა

ხრეშის თითოეული კენჭს უნდა ჰქონდეს ყველა მხარე ჩამოტეხილი, მოცულობითი წონა უნდა იყოს 1800 - 1900 კგ / მ 3.

შემავსებელი ქვიშა უნდა შედგებოდეს მკვრივი ნაწილაკებისაგან, არ უნდა შეიცავდეს თიხისა და მარილოვანი მინარევებს, და სხვა მავნე მინარევებს. ის უნდა, აკმაყოფილებდეს მცირე შემავსებლისა თვის წაყენებულ მოთხოვნებს.

### 4. ლითონის პროფილები

ლითონის მილკვადრატები უნდა აკმაყოფილებდეს Euronorm 19-57 სტანდარტს და დამატებით DIN 1025 Euronorm 19-57 (ზომები), EN 10034: 1993 (დაშვებები) და EN 10163-3, C (ზედაპირის ხარისხი), ლითონის ფურცელი უნდა აკმაყოფილებდეს სტანდარტს ГОСТ 103-76.

ლითონის ყველა ელემენტი დაიფაროს ანტიკოროზიული საღებავით . შედუღება უნდა განხორციელდეს E-42 ტიპის ელექტროდით

### 5. არმატურა

არმატურა რკინა-ბეტონის კონსტრუქციებში: პერიოდული Ø-12AIII, Ø-14AIII, Ø-18AIII, Ø-16AIII, 3400კგმ /სმ2 მაქსიმალური ზღვრული ძალით გაჭიმვაზე. საკიდისათვის Ø8, A I კლასის, მაქსიმალური ზღვრული ძალით გაჭიმვაზე 2100კგმ /სმ2 პროექტში გამოყენებული A I და AIII, კლასის არმატურა უნდა შესაბამებოდეს სტანდარტს ГОСТ 5781-82.

### 6. რულონური გაზონი

გაზონის ასაკი უნდა იყოს მინიმუმ 2 წელი, სარეველების გარეშე, მოჭრის სიმაღლე 4-5 სმ, მოჭრის სიგანე 45-50 სმ. ბალახის ღეროების სიხშირე დაახლოებით 50 ვცალი 10 სმ2-ზე. უნდა ქონდეს კარგად განვითარებული ფესვთა სისტემა.

### 7. ხის მასალა

ბანერის მოსაწყობად გამოყენებული ხის მასალა უნდა იყოს წიწვოვანი და ფოთლოვანი ჯიშის, ტენიანობის კოეფიციენტი-არაუმეტეს 20%-ისა. ( მშენებარე ობიექტზე ხის ტენიანობა განისაზღვრება სპეციალური ხელსაწყო დახმარებით. ) ხეს არ უნდა ჰქონდეს როკი - მთლიანი მოცულობის 10%-ზე მეტი და უნდა იყოს გარანდული.

კონსტრუქციაში გამოყენებამდე ხის მასალა დამუშავდეს ანტიბაქტერიალური და ხანძარსაწინააღმდეგო ხსნარით.

### 8. ანტიკოროზიული საღებავი

აკრილის ზეთოვანი ცვეთამდეგი საღებავი მაღალი ანტიკოროზიული მახასიათებლით. უნდა უზრუნველყოფდეს ულტრაიისფერი გამოსხივებისადმი მდგრადობას.

(ცვეთამედეგობის კლასი EN 13300)

## 9. ანტიესპტივი

ანტიესპტივი უნდა დაიცვას ხის მასალა ატმოსფერული ზემოქმედებისაგან, ღვრილის სოკოებისაგან, უნდა უზრუნველყოს ხანგრძლივი დაცვა ბიოდაზიანებისაგან.

## 10. ხის ლაქი

ხის ლაქი უნდა იყოს გარე გამოყენების, უნდა უზრუნველყოფდეს ორთქლგამტარობას, წყალმედეგობას, მექანიკური მოქმედებისადმი მედეგობას, ცვეთამედეგობას, ულტრაიისფერი გამოსხივებისადმი მდგრადობას.

### ხარისხის კონტროლი სამუშაოების შესრულების პროცესში

კონტრაქტორი პასუხისმგებელია შესრულებული სამუშაოების ხარისხზე მთელი სახელშეკრულებო ვადის განმავლობაში.

კონტრაქტორი და UNDP ინჟინერი სამუშაოების დაწყებამდე ათანხმებენ სამშენებლო-სამონტაჟო სამუშაოთა ხარისხის უზრუნველყოფის და მისი კონტროლის მეთოდებს, არსებული სამშენებლო ნორმებისა და წესების მოთხოვნების შესაბამისად.

ძირითადი სამშენებლო მასალების და აგრეგატების ობიექტზე შემოტანამდე, მოხდეს სანიმუშო ეგზემპლარის წარმოდგენა შესაბამისი სერტიფიკატით და მისი შეფასება

კომენტარები: კარ-ფანჯრების ბლოკების დამზადებამდე, კონტრაქტორმა უნდა მოახდინოს ღიობების ზუსტი გაზომვა. დაბალი ტემპერატურის შემთხვევაში ქვიშა-ცემენტის ხსნარში გამოყენებულ იქნეს პლასტიფიკატორები. სამშენებლო მასალები, ნივთები და აღჭურვილობა უნდა შეესაბამებოდეს საერთაშორისო სტანდარტებს და ეკოლოგიურ მოთხოვნებს და უნდა ჰქონდეს სათანადო მოწმობა.

სამშენებლო ნორმებისა და წესების (Snip-III-18-75 და Snip-III-4-80) მოთხოვნების მიხედვით უსაფრთხოების წესები მკაცრად უნდა იყოს დაცული.

სამშენებლო მასალები, ინსტრუმენტები და აღჭურვილობა უნდა აკმაყოფილებდეს საერთაშორისო სტანდარტებს, უნდა აკმაყოფილებდეს ეკოლოგიურ მოთხოვნებს და უნდა ჰქონდეს შესაბამისი სერტიფიკატი.

სამშენებლო მასალების ფერები უნდა იქნას შეთანხმებული დამკვეთთან და პროექტის ტექნიკურ ზედამხედველთან.

Annex II

**FORM FOR SUBMITTING SUPPLIER'S QUOTATION**  
*(This Form must be submitted only using the Supplier's Official Letterhead/Stationery<sup>1</sup>)*

We, the undersigned, hereby accept in full the UNDP General Terms and Conditions, and hereby offer to supply the works listed below in conformity with the specification and requirements of UNDP as per RFQ dated 18.05.2018

TABLE 1: Offer to Supply Services Compliant with Technical Specifications and Requirements

Rehabilitation of Machakhela National Park Administration and Visitor Centre Front Yard

მაჭახელას ეროვნული პარკის ადმინისტრაციის და ვიზიტორთა ცენტრის ეზოს კეთილმოწყობა

Bill of Quantities სამუშაოთა მოცულობის უწყისი

#	Works description სამუშაოთა დასახელება	Unit განზომილება	Quantity რაოდენობა	Materials მასალები		Wages ხელფასი		total GEL ჯამი	Country of production მწარმოებელი ქვეყანა	Brand's Name ბრენდის დასახელება
				Unit price ერთეულის ღირებ.	total GEL ჯამი	Unit Price ერთეულის ღირებ.	total GEL ჯამი			
1	2	3	4	5	6	7	8	9	10	11
1	Removing concrete covering on the wedge of retaining wall teritoriis gawmenda samSeneblo narCenebisagan, არსებული ბეტონის ნარჩენების საფარის მოხსნა საყრდენი კედლის ფერდზე	m <sup>2</sup>	120.00							
2	Disposing construction waste on landfill at 25 km in average სამშენებლო ნაგვის გატანა ნაგავსაყრელზე საშუალოდ 25 კმ მანძილზე	ton	20.00							

<sup>1</sup> Official Letterhead/Stationery must indicate contact details – addresses, email, phone and fax numbers – for verification purposes

3	Processing category III soil with excavator for foundation with 0.5 m3 clamshell III კატ. გრუნტის დამუშავება ექსკავატორით 0,5მ3 ჩამწით,	m <sup>3</sup>	24.10							
4	Arrangement of concrete under the spotted foundation with thickness 10cm. Concrete B-7.5 ბეტონის მომზადების მოწყობა ღობის კედლის ქვეშ, სისქით 10 სმ, ბეტონი ბ-7.5	m <sup>3</sup>	1.50							
5	Making formwork and dismantling for this monolithic concrete wall with formworks board 25 mm. რკინაბეტონის კედლისთვის ყალიბის მოწყობა და მოხსნა საყალიბე ფართით 25 მმ	m <sup>2</sup>	62.00							
6	Installation Wood plank grade II 60, 40 mm., for this concrete wall მონოლითური რკინაბეტონის კედლის ყალიბისთვის ფიცრის მონტაჟი II ხარ. 60, 40მმ	m <sup>3</sup>	0.40							
7	Installation of the armature grid for the monolithic concrete wall ( A-III class,D-16,12, mm. A-I class,D-8 ) მონოლითური რკინაბეტონის კედლისთვის არმატურის ბადის მონტაჟი (ა-IIIკლ. დ- 10, 12 მმ., ა-Iკლ. დ- 8მმ.)	ton	0.54							
8	Filling for the monolithic concrete wall with B-20 concrete მონოლითური რკინაბეტონის კედლისთვის ბეტონის მომზადება და შევსება B-20 კლ.ბეტონით	m <sup>3</sup>	14.20							
9	Arrangement of drainage pipe 50 mm. 35 cm სადრენაჟე მილების მონტაჟი 50 მმ, 35 სმ.	pc	8.00							
10	Arrangement of waterproofing with bitumen mastic ჰიდროიზოლაციის მოწყობა ბითუმის მასტისკით	m <sup>2</sup>	42.00							
11	Preparing of base with gravel under the water disposal, thickness 10cm სარინგლის ქვეშ საფუძვლის მომზადება სრემით სისქით 10სმ.	m <sup>3</sup>	1.50							
12	Arrangement of concrete blind area with B-15 concrete ბეტონის სარინგლის მოწყობა B-15 კლ.ბეტონით	m <sup>3</sup>	1.50							



13	Backfilling with hand უკუხაყრა ხელით	გრუნტის	m <sup>3</sup>	20.00									
14	Installation Fence of metal elements - square pipes 120X120X3 mm. მილკვადრატების 120*120*3 მმ მონტაჟი ღობისთვის		m	32.95									
15	Installation Fence and gates of metal elements - square pipes 80X80X3 mm. მილკვადრატების 80*80*3 მმ მონტაჟი ღობისთვის და კუტიკარისთვის		m	143.36									
16	Installation Fence and gates of metal elements - square pipes 40X40X2 mm. მილკვადრატების 40*40*2 მმ მონტაჟი ღობისთვის და კუტიკარისთვის		m	146.96									
17	Installation metal sheet 200*200* 4 mm. for the anchor ლითონის ფურცლის მონტაჟი 200*200*4 მმ. ანკერისთვის		pc	29.00									
18	Anchor 8 mm. 10 cm. for the metal sheet ლითონის ფურცლისთვის 8 მმ. 10 სმ.	ანკერი	pc	116.00									
19	Installation metal sheet 120*120* 3 mm. on the fences pillar ლითონის ფურცლის მონტაჟი 120*120*3 ღობის დგარებზე		pc	29.00									
20	Installation lock for the gates მოწყობა კუტიკარისთვის	საკეტის	pc	3.00									
21	Arrangement drainage layer with Crushed stone ღორღის შემოტანა სადრენაჟე ფენის მოსაწობად.		m <sup>3</sup>	10.00									
22	Ground transportation by truck pavement with Bulldozer and compacting გრუნტის შემოტანა სატვირთო მანქანით, მოსწორება ბულდოზერით და დატკეპნა		m <sup>3</sup>	180.00									

23	Making and processing with anticorrosive paint fences metal elements ღობის ლითონის ელემენტების დამუშავება და შეღებვა ანტიკოროზიული საღებავით	m <sup>2</sup>	83.50							
24	Splashing fences walls with sand cement emulsion ღობის კედლების დაშხეფვა ქვიშა-ცემენტის ხსნარით დეკორატიული ცემენტის გამოყენებით	m <sup>2</sup>	80.00							
25	Arrangement of concrete socle with B-20 concrete length 20 m. ბეტონის ცოკლის მოწყობა B-20 კლ.ბეტონით სიგრძე 20 მ.	m <sup>3</sup>	1.50							
26	Arrangement of concrete blind area on the retaining wall with B-15 concrete, length 14 m. ბეტონის სარინელის მოწყობა საყრდენ კედელთან B-15 კლ.ბეტონით, სიგრძე 14 მ.	m <sup>3</sup>	1.50							
27	Installation of the armature grid for the monolithic concrete platform ( A-I class,D-8 ) მონოლითური რკინაბეტონის ფილისთვის არმატურის ბადის მონტაჟი (ა-I კლ. დ- 8მმ.)	ton	0.08							
28	Filling for the monolithic concrete platform with B-20 concrete მონოლითური რკინაბეტონის ფილისთვის ბეტონის მომზადება და შევსება B-20 კლ.ბეტონით	m <sup>3</sup>	1.40							
29	Ground processing for grass cover გრუნტის დამუშავება ბალახის საფარის მოსაწყობად	m <sup>2</sup>	170.00							
30	Arrangement of grass cover (rolling lawn) ბალახის საფარის მოწყობა (რულონური გაზონი)	m <sup>2</sup>	170.00							
31	Arrangement of sand cover for concrete path ბეტონის ბილიკისთვის ქვიშის საფარის მოწყობა	m <sup>2</sup>	32.50							
32	Laying with artificial concrete tiles ხელოვნური ბეტონის ფილებით მომზადება	m <sup>2</sup>	32.50							

33	Making of border stone with concrete blocks 5X30X60cm along the road მოშანდაკებული გზის გასწვრის ბორდიურის მონტაჟი ბეტონის ბლოკებით 5X30X60სმ.	m	36.00							
34	Seeding grass on the wedge of retaining wall (ground processing) საყრდენი კედლის ფერდზე გრუნტის დამუშავება და ბალახის დათესვა	m <sup>2</sup>	120.00							
35	Installation of a square metal benches, with concreting of pillars (design/color to be agreed with client) სკვერის ლითონის სკამის მონტაჟი ფეხების დაბეტონებით (დიზაინი და ფერი შეთანხმდეს დამკვეთთან)	pc	3.00							
36	Installation of a square urn, (closed type) with concreting of pillars (design/color to be agreed with client) ურნების (დახურული ტიპის) მონტაჟი, დგარების დაბეტონებით (დიზაინი და ფერი შეთანხმდეს დამკვეთთან)	pc	3.00							
37	Blackout the fiberglass walls and roof with a dark tone membrane (color to be agreed with client) კიბის უჯრედის შემინული კედლების და სახურავის დაბურვა მუქი ტონალობის ფირით (ფერი შეთანხმდეს დამკვეთთან)	m <sup>2</sup>	61.95							
38	Installation a bicycle parking at 10 bicycles with square pipes 60X40X3 mm. and metal pipes 40 mm. (concreting 4 points) ველოსიპედის სადგომის მოწყობა 10 ცალ ველოსიპედზე მილკვადრატით 60*40*3 მმ. და მრგვალი მილით 40 მმ. (ნაბეტონება 4 წერტილში)	m	8.00							
39	Making and processing with anticorrosive paint bicycle parkings metal elements ველოპარკინგის ლითონის ელემენტების დამუშავება და შეღებვა ანტიკოროზიული საღებავით	m	8.00							
40	The inscription on the facade, thickness 8 cm, height, 100 cm " i " (see render ) სახურავის კეხთან ბარელიეფური წარწერის მოწყობა სარეკლამო მოცულობითი ასობით სისქე 8სმ სიმაღლე 100 სმ " i "	pc	1.00							
41	Installation pillars of metal elements - square pipes 100X100X4 mm. for the banner ლითონის კვადრატული მილით 100*100*4 ბანერის დგარების მოწყობა	m	10.00							
42	Concreting metal pillars for the banners depth 80 cm, in 3 points ბანერის ლითონის დგარების დაბეტონება 0.8 მ. სიღრმის ორმოში 3 წერტილში.	m <sup>3</sup>	0.50							

43	Arrangement of banners with a guaranteed wooden plank, (coniferous material) thickness 5 cm, width 20 cm. ბანერის მოწყობა გარანდული ფიცრით (წიწვოვანი მასალა) სისქე 5 სმ, სიგანე 20 სმ.	m <sup>2</sup>	11.00							
44	Arrangement of banners with a guaranteed wooden log, (deciduous material) 20 cm. ბანერისთვის ხის კარკასის მოწყობა მრგვალი მორებით 20 სმ. (ფოთლოვანი მასალა)	m <sup>3</sup>	0.90							
45	Processing wooden surface with Antibacterial and fire prevention solution ხის ზედაპირის დამუშავება ანტიბაქტერიული და ხანძარსაწინააღმდეგო ხსნარით	m <sup>2</sup>	35.00							
46	Processing wooden surface with varnish (two layer) ხის ზედაპირის დამუშავება ლაკით, ორი პირი	m <sup>2</sup>	35.00							
47	Making and processing with anticorrosive paint banners metal elements ბანერის ლითონის ელემენტების დამუშავება და შეღებვა ანტიკოროზიული საღებავით	m <sup>2</sup>	4.00							
48	Arrangement inscription of banner with polypropylene material bilingual (Machakhela National Park) ბანერზე წარწერის მოწყობა პოლიპროპილენის მასალისაგან ორენოვანი (მაჭახელას ეროვნული პარკი, )	set	1.00							
49	Arranging the logo on the banner with polypropylene material diameter 1.0 m. (See the design in the specification) ბანერზე ლოგოს მოწყობა პოლიპროპილენის მასალისაგან დიამეტრით 1.0 მ. (დიზაინი იხილეთ სპეციფიკაციაში)	set	1.00							
50	Disposing construction waste on landfill at 25 km in average სამშენებლო ნაგვის გატანა ნაგავსაყრელზე საშუალოდ 25 კმ მანძილზე	ton	10.00							

	<b>Total</b> ჯამი									
	Transportation expenses (material resources) სატრანსპორტო ხარჯები (მატერიალური რესურსიდან)									
	<b>Total</b> ჯამი									
	Overhead expenses ზედნადები ხარჯები									
	<b>Total</b> ჯამი									
	Planned Profit გეგმიური ღირებულება									
	<b>Total</b> ჯამი									
	Unforeseen expenses გაუთვალისწინებელი ხარჯები									
	<b>Total</b> ჯამი									

**TABLE 2 - Work experience as a prime contractor over the last 3 years. List of performed projects is to be split by years. Each year is to be started with total amount of the year.**

Provide background of the company with supporting documents (company registration)

**Year of establishment:**

**Registration No, and place:**

**Tax certificate:**

**Power of Attorney for signatory of the Quotation:**

#	Project Name	Name of Employer	Description of work	Contract amount (USD)	Period of completion	Contact person
	<b>2016</b>					
1						
2						
3						
4						
5						
	<b>2017</b>					
1						
2						
3						
4						
5						

Director:

**TABLE 3 - List of Key Personnel Proposed for the Project**

#	Name of Personnel	Proposed Position	Qualification	Work Experience (Years) in	
				Related to Work	Total
1					
2					
3					
4					
5					
6					
7					
8					
9					
10					
11					
12					
13					
14					
15					

Director:

**TABLE 4 – PROGRESS SCHEDULE OF THE PROJECT COMPANY**

№	Type of work	Month 1				Month 2			
		Week 1	Week 2	Week 3	Week 4	Week 1	Week 2	Week 3	Week 4
1									
2									
3									
4									
5									
6									
7									
Schedule of the labour power									

**Total number of days relevant to the project** \_\_\_\_\_

**Date:**

**Signature:**

**Seal:**



**TABLE 5: List of equipment and machinery to be used:**

<u>No</u>	<u>Equipment and Machinery</u>	
<u>1</u>		
<u>2</u>		
<u>3</u>		
<u>4</u>		

**TABLE 6: Offer to Comply with Other Conditions and Related Requirements**

Other Information pertaining to our Quotation are as follows :	Your Responses		
	<i>Yes, we will comply</i>	<i>No, we cannot comply</i>	<i>If you cannot comply, pls. indicate counter proposal</i>
Validity of Quotation 60 days			
All Provisions of the UNDP General Terms and Conditions			
Compliance with Liquidated Damages			
Compliance with warranty condition			
Compliance with Technical Specifications			

All other information that we have not provided automatically implies our full compliance with the requirements, terms and conditions of the RFQ.

*[Name and Signature of the Supplier's Authorized Person]*  
*[Designation]*  
*[Date]*



*Empowered lives.  
Resilient nations.*

## General Terms and Conditions for Civil Works

1. Definitions
2. Singular and Plural
3. Headings or Notes
4. Legal Relationships
5. General Duties/Powers of Engineer
6. Contractor's General Obligations/Responsibilities
7. Assignment and Subcontracting
8. Drawings
9. Work Book
10. Performance Security
11. Inspection of Site
12. Sufficiency of Tender
13. Programme of Work to be Furnished
14. Weekly Site Meeting
15. Change Orders
16. Contractor's Superintendence
17. Contractor's Employees
18. Setting-Out
19. Watching and Lighting
20. Care of Works
21. Insurance of Works, Etc.
22. Damage to Persons and Property
23. Liability Insurance
24. Accident or Injury to Workmen
25. Remedy on Contractor's Failure to Insure
26. Compliance with Statutes, Regulations, Etc.
27. Fossils, Etc.
28. Copyright, Patents and Other Proprietary Rights, and Royalties
29. Interference With Traffic and Adjoining Properties
30. Extraordinary Traffic and Special Loads
31. Opportunities for Other Contractors
32. Contractor to Keep Site Clean
33. Clearance of Site on Substantial Completion
34. Labour
35. Returns of Labour, Plant, Etc.
36. Materials, Workmanship and Testing
37. Access to Site

38. Examination of Work Before Covering Up
39. Removal of Improper Work and Materials
40. Suspension of Work
41. Possession of Site
42. Time for Completion
43. Extension of Time for Completion
44. Rate of Progress
45. Liquidated Damages for Delay
46. Certificate of Substantial Completion
47. Defects Liability
48. Alterations, Additions and Omissions
49. Plant, Temporary Works and Materials
50. Approval of Materials, Etc., Not Implied
51. Measurement of Works
52. Liability of the Parties
53. Authorities
54. Urgent Repairs
55. Increase and Decrease of Costs
56. Taxation
57. Blasting
58. Machinery
59. Temporary Works and Reinstatement
60. Photographs and Advertising
61. Prevention of Corruption
62. Date Falling on Holiday
63. Notices
64. Language, Weights and Measures
65. Records, Accounts, Information and Audit
66. Force Majeure
67. Suspension by the UNDP
68. Termination by the UNDP
69. Termination by the Contractor
70. Rights and Remedies of the UNDP
71. Settlement of Disputes
72. Privileges and Immunities

Appendix I: Formats of Performance Security  
Performance Bank Guarantee  
Performance Bond

## **DEFINITIONS**

For the purpose of the Contract Documents the words and expressions below shall have the following meanings:

- a) "Employer" means the United Nations Development Programme (UNDP).
- b) "Contractor" means the person whose tender has been accepted and with whom the Contract has been entered into.

- c) "Engineer" means the person whose services have been engaged by UNDP to administer the Contract as provided therein, as will be notified in writing to the Contractor.
- d) "Contract" means the written agreement between the Employer and the Contractor, to which these General Conditions are annexed.
- e) "The Works" means the works to be executed and completed under the Contract.
- f) "Temporary Works" shall include items to be constructed which are not intended to be permanent and form part of the Works.
- g) "Drawings" and "Specifications" mean the Drawings and Specifications referred to in the Contract and any modification thereof or addition thereto furnished by the Engineer or submitted by the Contractor and approved in writing by the Engineer in accordance with the Contract.
- h) "Bill of Quantities" is the document in which the Contractor indicates the cost of the Works, on the basis of the foreseen quantities of items of work and the fixed unit prices applicable to them.
- i) "Contract Price" means the sum agreed in the Contract as payable to the Contractor for the execution and completion of the Works and for remedying of any defects therein in accordance with the Contract.
- j) "Site" means the land and other places on, under, in or through which the Works or Temporary Works are to be constructed.

#### **SINGULAR AND PLURAL**

Words importing persons or parties shall include firms or companies and words importing the singular only shall also include the plural and vice versa where the context requires.

#### **HEADINGS OR NOTES**

The headings or notes in the Contract Documents shall not be deemed to be part thereof or be taken into consideration in their interpretation.

#### **LEGAL RELATIONSHIPS**

The Contractor and the sub-contractor(s), if any, shall have the status of an independent contractor vis-à-vis the Employer. The Contract Documents shall not be construed to create any contractual relationship of any kind between the Engineer and the Contractor, but the Engineer shall, in the exercise of his duties and powers under the Contract, be entitled to performance by the Contractor of its obligations, and to enforcement thereof. Nothing contained in the Contract Documents shall create any contractual relationship between the Employer or the Engineer and any subcontractor(s) of the Contractor.

#### **GENERAL DUTIES/POWERS OF ENGINEER**

- a) The Engineer shall provide administration of Contract as provided in the Contract Documents. In particular, he shall perform the functions hereinafter described.
- b) The Engineer shall be the Employer's representative vis-à-vis the Contractor during construction and until final payment is due. The Engineer shall advise and consult with the Employer. The Employer's instructions to the Contractor shall be forwarded through the Engineer. The Engineer shall have authority to act on behalf of the Employer only to the extent provided in the Contract Documents as they may be amended in writing in accordance with the Contract. The duties, responsibilities and limitations of authority of the Engineer as the Employer's representative during construction as set forth in the Contract shall not be modified or extended without the written consent of the Employer, the Contractor and the Engineer.
- c) The Engineer shall visit the Site at intervals appropriate to the stage of construction to familiarize himself generally with the progress and quality of the Works and to determine in general if the Works are proceeding in accordance with the Contract Documents. On the basis of his on-site observations as an Engineer, he shall keep the Employer informed of the progress of the Works.
- d) The Engineer shall not be responsible for and will not have control or charge of construction means, methods, techniques, sequences or procedures, or for safety precautions and programs in connection with the Works or the Temporary Works. The Engineer shall not be responsible for or have control or charge over the acts or omissions of the Contractor (including the Contractor's failure to carry out the Works in accordance with the Contract) and of Sub-contractors or any of their agents or employees, or any other persons performing services for the Works, except if such acts or omissions are caused by the Engineer's failure to perform his functions in accordance with the contract between the Employer and the Engineer.
- e) The Engineer shall at all times have access to the Works wherever and whether in preparation or progress. The Contractor shall provide facilities for such access so that the Engineer may perform his functions under the Contract.
- f) Based on the Engineer's observations and an evaluation of the documentation submitted by the Contractor together with the invoices, the Engineer shall determine the amounts owed to the Contractor and shall issue Certificates for Payment as appropriate.
- g) The Engineer shall review and approve or take other appropriate action upon the Contractor's submittals such as Shop Drawings, Product Data and Samples, but only for conformity with the design concept of the Works and with the provisions of the Contract Documents. Such action shall be taken with reasonable promptness so as to cause no delay. The Engineer's approval of a specific item shall not indicate approval of an assembly of which the item is a component.
- h) The Engineer shall interpret the requirements of the Contract Documents and judge the performance thereunder by the Contractor. All interpretations and orders of the Engineer shall be consistent with the intent of and reasonably inferable from the Contract Documents and shall be in writing or in the form of drawings. Either party may make a written request to the Engineer for such interpretation. The Engineer shall render the interpretation necessary for the proper execution of the Works with reasonable promptness and in accordance with any time limit agreed upon. Any claim or dispute arising from the interpretation of the Contract Documents by the Engineer or relating to the execution or progress of the Works shall be settled as provided in Clause 71 of these General Conditions.

- i) Except as otherwise provided in the Contract, the Engineer shall have no authority to relieve the Contractor of any of his obligations under the Contract nor to order any work involving delay in completion of the Works or any extra payment to the Contractor by the Employer, or to make any variations to the Works.
- j) In the event of termination of the employment of the Engineer, the Employer shall appoint another suitable professional to perform the Engineer's duties.
- k) The Engineer shall have authority to reject work which does not conform to the Contract Documents. Whenever, in his opinion, he considers it necessary or advisable for the implementation of the intent of the Contract Documents, he will have authority to require special inspection or testing of the work whether or not such work be then fabricated, installed or completed. However, neither the Engineer's authority to act nor any reasonable decision made by him in good faith either to exercise or not to exercise such authority shall give rise to any duty or responsibility of the Engineer to the Contractor, any subcontractor, any of their agents or employees, or any other person performing services for the Works.
- l) The Engineer shall conduct inspections to determine the dates of Substantial Completion and Final Completion, shall receive and forward to the Employer for the Employer's review written warranties and related documents required by the Contract and assembled by the Contractor, and shall issue a final Certificate for Payment upon compliance with the requirements of Clause 47 hereof and in accordance with the Contract.
- m) If the Employer and Engineer so agree, the Engineer shall provide one or more Engineer's Representative(s) to assist the Engineer in carrying out his responsibilities at the site. The Engineer shall notify in writing to the Contractor and the Employer the duties, responsibilities and limitations of authority of any such Engineer's Representative(s).

## **CONTRACTOR'S GENERAL OBLIGATIONS/RESPONSIBILITIES**

### **6.1. Obligation to Perform in Accordance with Contract**

The Contractor shall execute and complete the Works and remedy any defects therein in strict accordance with the Contract, with due care and diligence and to the satisfaction of the Engineer, and shall provide all labor, including the supervision thereof, materials, Constructional Plant and all other things, whether of a temporary or permanent nature, required in and for such execution, completion and remedying of defects, as far as the necessity for providing the same is specified in or is reasonably to be inferred from the Contract. The Contractor shall comply with and adhere strictly to the Engineer's instructions and directions on any matter, touching or concerning the Works.

### **6.2 Responsibility for Site Operations**

The Contractor shall take full responsibility for the adequacy, stability and safety of all site operations and methods of construction, provided that the Contractor shall not be responsible, except as may be expressly provided in the Contract, for the design or specification of the Permanent Works or of any Temporary Works prepared by the Engineer.

### **6.3. Responsibility for Employees**

The Contractor shall be responsible for the professional and technical competence of his employees and will select for work under this Contract, reliable individuals who will perform effectively in the implementation of the Contract, respect local customs and conform to a high standard of moral and ethical conduct.

### **6.4. Source of Instructions**

The Contractor shall neither seek nor accept instructions from any authority external to the Employer, the Engineer or their authorized representatives in connection with the performance of his services under this Contract. The Contractor shall refrain from any action which may adversely affect the Employer and shall fulfill his commitments with fullest regard for the interest of the Employer.

### **6.5. Officials Not to Benefit**

The Contractor warrants that no official of the Employer has been or shall be admitted by the Contractor to any direct or indirect benefit arising from this Contract or the award thereof. The Contractor agrees that breach of this provision is a breach of an essential term of the Contract.

### **6.6. Use of Name, Emblem or Official Seal of UNDP or the United Nations**

The Contractor shall not advertise or otherwise make public the fact that he is performing, or has performed services for the Employer or use the name, emblem or official seal of the Employer or the United Nations or any abbreviation of the name of the Employer or the United Nations for advertising purposes or any other purposes.

### **6.7. Confidential Nature of Documents**

All maps, drawings, photographs, mosaics, plans, reports, recommendations, estimates, documents and all other data compiled by or received by the Contractor under the Contract shall be the property of the Employer, shall be treated as confidential and shall be delivered only to the duly authorized representative of the Employer on completion of the Works; their contents shall not be made known by the Contractor to any person other than the personnel of the Contractor performing services under this Contract without the prior written consent of the Employer.

## **ASSIGNMENT AND SUBCONTRACTING**

### **7.1. Assignment of Contract**

The Contractor shall not, except after obtaining the prior written approval of the Employer, assign, transfer, pledge or make other disposition of the Contract or any part thereof or of any of the Contractor's rights, claims or obligations under the Contract.

### **7.2. Subcontracting**

In the event the Contractor requires the services of subcontractors, the Contractor shall obtain the prior written approval of the Employer for all such subcontractors. The approval of the Employer



shall not relieve the Contractor of any of his obligations under the Contract, and the terms of any subcontract shall be subject to and be in conformity with the provisions of the Contract.

### **7.3. Assignment of Subcontractor's Obligations**

In the event of a subcontractor having undertaken towards the Contractor in respect of the work executed or the goods, materials, Plant or services supplied by such subcontractor for the Works, any continuing obligation extending for a period exceeding that of the Defects Liability Period under the Contract, the Contractor shall at any time after the expiration of such Period, assign to the Employer, at the Employer's request and cost, the benefit of such obligation for the unexpired duration thereof.

## **DRAWINGS**

### **8.1. Custody of drawings**

The drawings shall remain in the sole custody of the Employer but two (2) copies thereof shall be furnished to the Contractor free of cost. The Contractor shall provide and make at his own expense any further copies required by him. At the completion of the Works, the Contractor shall return to the Employer all drawings provided under the Contract.

### **8.2. One copy of Drawings to be kept on Site**

One copy of the Drawings furnished to the Contractor as aforesaid shall be kept by the Contractor on the Site and the same shall at all reasonable times be available for inspection and use by the Engineer and by any other person authorized in writing by the Engineer.

### **8.3. Disruption of Progress**

The Contractor shall give written notice to the Engineer whenever planning or progress of the Works is likely to be delayed or disrupted unless any further drawing or order, including a direction, instruction or approval, is issued by the Engineer within a reasonable time. The notice shall include details of drawing or order required and of why and by when it is required and of any delay or disruption likely to be suffered if it is late.

## **WORK BOOK**

The Contractor shall maintain a Work Book at the Site with numbered pages, in one original and two copies. The Engineer shall have full authority to issue new orders, drawings and instructions to the Contractor, from time to time and as required for the correct execution of the Works. The Contractor shall be bound to follow such orders, drawings and instructions.

Every order shall be dated and signed by the Engineer and the Contractor, in order to account for its receipt.

Should the Contractor want to refuse an order in the Work Book, he shall so inform the Employer, through the Engineer, by means of an annotation in the Work Book made within three (3) days from

the date of the order that the Contractor intends to refuse. Failure by the Contractor to adhere to this procedure shall result in the order being deemed accepted with no further possibility of refusal.

The original of the Work Book shall be delivered to the Employer at the time of Final Acceptance of the Works. A copy shall be kept by the Engineer and another copy by the Contractor.

## **PERFORMANCE SECURITY**

- a) As guarantee for his proper and efficient performance of the Contract, the Contractor shall on signature of the Contract furnish the Employer with a Performance Security issued for the benefit of the Employer. The amount and character of such security (bond or guarantee) shall be as indicated in the Contract.
- b) The Performance Bond or Bank Guarantee must be issued by an acceptable insurance company or accredited bank, in the format included in Appendix I to these General Conditions, and must be valid up to twenty-eight days after issuance by the Engineer of the Certificate of Final Completion. The Performance Bond or Bank Guarantee shall be returned to the Contractor within twenty-eight days after the issuance by the Engineer of the Certificate of Final Completion, provided that the Contractor shall have paid all money owed to the Employer under the Contract.
- c) If the surety of the Performance Bond or Bank Guarantee is declared bankrupt or becomes insolvent or its right to do business in the country of execution of the Works is terminated, the Contractor shall within five (5) days thereafter substitute another bond or guarantee and surety, both of which must be acceptable to the Employer.

## **11. INSPECTION OF SITE**

The Contractor shall be deemed to have inspected and examined the site and its surroundings and to have satisfied himself before submitting his Tender and signing the Contract as to all matters relative to the nature of the land and subsoil, the form and nature of the Site, details and levels of existing pipe lines, conduits, sewers, drains, cables or other existing services, the quantities and nature of the work and materials necessary for the completion of the Works, the means of access to the Site, and the accommodation he may require, and in general to have himself obtained all necessary information as to risk contingencies, climatic, hydrological and natural conditions and other circumstances which may influence or affect his Tender, and no claims will be entertained in this connection against the Employer.

## **12. SUFFICIENCY OF TENDER**

The Contractor shall be deemed to have satisfied himself before tendering as to the correctness and sufficiency of his Tender for the construction of the Works and of the rates and prices, which rates and prices shall, except in so far as it is otherwise provided in the Contract, cover all his obligations under the Contract and all matters and things necessary for the proper execution and completion of the Works.

## **13. PROGRAMME OF WORK TO BE FURNISHED**

Within the time limit specified in the Contract, the Contractor shall submit to the Engineer for his consent a detailed Programme of Work showing the order of procedure and the method in which

he proposes to carry out the Works. In preparing his Programme of Work the Contractor shall pay due regard to the priority required by certain works. Should the Engineer, during the progress of work, require further modifications to the Programme of Work, the Contractor shall review the said program. The Contractor shall also whenever required by the Engineer submit particulars in writing of the Contractor's arrangements for carrying out the Works and of the Constructional Plant and Temporary Works which the Contractor intends to supply, use or construct as the case may be. The submission of such program, or any modifications thereto, or the particulars required by the Engineer, shall not relieve the Contractor of any of his duties or obligations under the Contract nor shall the incorporation of any modification to the Programme of Work either at the commencement of the contract or during its course entitle the Contractor to any additional payments in consequence thereof.

### **WEEKLY SITE MEETING**

A weekly site meeting shall be held between the UNDP Project Coordinator or engineer, if any, the representative of the Contractor and the Engineer or the Engineer's Representative, in order to verify that the Works are progressing normally and are executed in accordance with the Contract.

### **CHANGE ORDERS**

- a) The Engineer may instruct the Contractor, with the approval of the Employer and by means of Change Orders, all variations in quantity or quality of the Works, in whole or in part, that are deemed necessary by the Engineer.
- b) Processing of change orders shall be governed by clause 48 of these General Conditions.

### **CONTRACTOR'S SUPERINTENDENCE**

The Contractor shall provide all necessary superintendence during the execution of the Works and as long thereafter as the Engineer may consider necessary for the proper fulfillment of the Contractor's obligations under the Contract. The Contractor or a competent and authorized agent or representative of the Contractor approved in writing by the Engineer, which approval may at any time be withdrawn, shall be constantly on the site and shall devote his entire time to the superintendence of the Works. Such authorized agent or representative shall receive on behalf of the Contractor directions and instructions from the Engineer. If the approval of such agent or representative shall be withdrawn by the Engineer, as provided in Clause 17(2) hereinafter, or if the removal of such agent or representative shall be requested by the Employer under Clause 17(3) hereinafter, the Contractor shall as soon as it is practicable after receiving notice of such withdrawal remove the agent or representative from the Site, and replace him by another agent or representative approved by the Engineer. Notwithstanding the provision of Clause 17(2) hereinafter, the Contractor shall not thereafter employ, in any capacity whatsoever, a removed agent or representative again on the Site.

### **CONTRACTOR'S EMPLOYEES**

- a) The Contractor shall provide and employ on the Site in connection with the execution and completion of the Works and the remedying of any defects therein:

- i. Only such technical assistants as are skilled and experienced in their respective callings and such sub-agent foremen and leading hands as are competent to give proper supervision to the work they are required to supervise, and
  - ii. Such skilled, semi-skilled, and unskilled labour as is necessary for the proper and timely execution and completion of the Works.
- b) The Engineer shall be at liberty to object to and require the Contractor to remove forthwith from the Works any person employed by the Contractor in or about the execution or completion of the Works, who in the opinion of the Engineer is misconducting himself, or is incompetent or negligent in the proper performance of his duties, or whose employment is otherwise considered reasonably by the Engineer to be undesirable, and such person shall not be again employed on the Site without the written permission of the Engineer. Any person so removed from the Works shall be replaced as soon as reasonably possible by a competent substitute approved by the Engineer.
  - c) Upon written request by the Employer, the Contractor shall withdraw or replace from the Site any agent, representative or other personnel who does not conform to the standards set forth in paragraph (1) of this Clause. Such request for withdrawal or replacement shall not be considered as termination in part or in whole of this Contract. All costs and additional expenses resulting from any withdrawal or replacement for whatever reason of any of the Contractor's personnel shall be at the Contractor's expense.

#### **SETTING-OUT**

The Contractor shall be responsible for the true and proper setting out of the Works in relation to original points, lines and levels of reference given by the Engineer in writing and for the correctness of the position, levels, dimensions and alignment of all parts of the Works and for the provision of all necessary instruments, appliances and labor in connection therewith. If, at any time during the progress of the Works, any error shall appear or arise in the position, levels, dimensions or alignment of any part of the Works, the Contractor, on being required so to do by the Engineer, shall, at his own cost, rectify such error to the satisfaction of the Engineer.

#### **WATCHING AND LIGHTING**

The Contractor shall in connection with the Works provide and maintain at his own cost all lights, guards, fencing and watching when and where necessary or required by the Engineer or by any duly constituted authority for the protection of the Works and the materials and equipment utilized therefor or for the safety and convenience of the public or others.

#### **CARE OF WORKS**

- a) From the commencement date of the Works to the date of substantial completion as stated in the Certificate of Substantial Completion, the Contractor shall take full responsibility for the care thereof and of all Temporary Works. In the event that any damage or loss should happen to the Works or to any part thereof or to any Temporary Works from any cause whatsoever (save and except as shall be due to Force Majeure as defined in Clause 66 of these General Conditions), the Contractor shall at his own cost repair and make good the same so that, at completion, the Works shall be in good order and condition and in conformity in every respect with the requirements of the Contract and the Engineer's instructions. The Contractor shall also be liable for any damage to the

Works occasioned by him in the course of any operations carried out by him for the purpose of complying with his obligations Clause 47 hereof.

- b) The Contractor shall be fully responsible for the review of the Engineering design and details of the Works and shall inform the Employer of any mistakes or incorrectness in such design and details which would affect the Works.

### **INSURANCE OF WORKS, ETC.**

Without limiting his obligations and responsibilities under Clause 20 hereof, the Contractor shall insure immediately following signature of this Contract, in the joint names of the Employer and the Contractor (a) for the period stipulated in Clause 20(1) hereof, against all loss or damage from whatever cause arising, other than cause of Force majeure as defined in clause 66 of these General Conditions, and (b) against loss or damage for which the Contractor is responsible, in such manner that the Employer and the Contractor are covered for the period stipulated in Clause 20 (1) hereof and are also covered during the Defects Liability Period for loss or damage arising from a cause occurring prior to the commencement of the Defects Liability Period and for any loss or damage occasioned by the Contractor in the course of any operations carried out by him for the purpose of complying with his obligations under Clause 47 hereof:

- a) The Works, together with the materials and Plant for incorporation therein, to their full replacement cost, plus an additional sum of ten (10) per cent of such replacement cost, to cover any additional costs of and incidental to the rectification of loss or damage including professional fees and the cost of demolishing and removing any part of the Works and of removing debris of whatsoever nature;
- b) The Contractor's equipment and other things brought on to the Site by the Contractor to the replacement value of such equipment and other things;
- c) An insurance to cover the liabilities and warranties of Section 52(4);

Such insurance shall be effected with an insurer and in terms approved by the Employer, which approval shall not be unreasonably withheld, and the Contractor shall, whenever required, produce to the Engineer the policy or policies of insurance and the receipts for payment of the current premiums.

### **DAMAGE TO PERSONS AND PROPERTY**

The Contractor shall (except if and so far as the Contract provides otherwise) indemnify, hold and save harmless and defend at his own expense the Employer, its officers, agents, employees and servants from and against all suits, claims, demands, proceedings, and liability of any nature or kind, including costs and expenses, for injuries or damages to any person or any property whatsoever which may arise out of or in consequence of acts or omissions of the Contractor or its agents, employees, servants or subcontractors in the execution of the Contract. The provision of this Clause shall extend to suits, claims, demands, proceedings and liability in the nature of workmen's compensation claims and arising out of the use of patented inventions and devices. Provided always that nothing herein contained shall be deemed to render the Contractor liable for or in respect of or with respect to:

- a) The permanent use or occupation of land by the Works or any part thereof;
- b) The right of the Employer to construct the Works or any part thereof on, over, under, or through any land.
- c) Interference whether temporary or permanent with any right of light, airway or water or other easement or quasi-easement which is the unavoidable result of the construction of the Works in accordance with the Contract.
- d) Death, injuries or damage to persons or property resulting from any act or neglect of the Employer, his agents, servants or other contractors, done or committed during the validity of the Contract.

## **LIABILITY INSURANCE**

### **23.1. Obligation to take out Liability Insurance**

Before commencing the execution of the Works, but without limiting his obligations and responsibility under Clause 20 hereof, the Contractor shall insure against his liability for any death, material or physical damage, loss or injury which may occur to any property, including that of the Employer or to any person, including any employee of the Employer by or arising out of the execution of the Works or in the carrying out of the Contract, other than due to the matters referred to in the proviso to Clause 22 hereof.

### **23.2. Minimum Amount of Liability Insurance**

Such insurance shall be effected with an insurer and in terms approved by the Employer, which approval shall not be unreasonably withheld, and for at least the amount specified in the contract. The Contractor shall, whenever required by the Employer or the Engineer, produce to the Engineer the policy or policies of insurance and the receipts for payment of the current premiums.

### **23.3. Provision to Indemnify Employer**

The insurance policy shall include a provision whereby, in the event of any claim in respect of which the Contractor would be entitled to receive indemnity under the policy, being brought or made against the Employer, the insurer shall indemnify the Employer against such claims and any costs, charges and expenses in respect thereof.

## **ACCIDENT OR INJURY TO WORKMEN**

- a) The Employer shall not be liable for or in respect of any damages or compensation payable at law in respect or in consequence of any accident or injury to any workman or other person in the employment of the Contractor or any sub-Contractor, save and except an accident or injury resulting from any act or default of the Employer, his agents or servants. The Contractor shall indemnify, hold and save harmless the Employer against all such damages and compensation, save and except as aforesaid, and against all claims, proceedings, costs, charges and expenses whatsoever in respect thereof or in relation thereto.
- b) Insurance Against Accident, etc., to Workmen

The Contractor shall insure against such liability with an insurer approved by the Employer, which approval shall not be unreasonably withheld, and shall continue such insurance during the whole of the time that any persons are employed by him for the Works and shall, when required, produce to the Engineer such policy of insurance and the receipt for payment of the current premium. Provided always that, in respect of any persons employed by any subcontractor, the Contractor's obligation to insure as aforesaid under this sub-clause shall be satisfied if the subcontractor shall have insured against the liability in respect of such persons in such manner that the Employer is indemnified under the policy but the Contractor shall require such subcontractor to produce to the Engineer when required such policy of insurance and the receipt for the current premium, and obtain the insertion of a provision to that effect in its contract with the subcontractor.

#### **REMEDY ON CONTRACTOR'S FAILURE TO INSURE**

If the Contractor shall fail to effect and keep in force any of the insurances referred to in Clauses 21, 23 and 24 hereof, or any other insurance which he may be required to effect under the terms of the Contract, the Employer may in any such case effect and keep in force any such insurance and pay such premium as may be necessary for that purpose and from time to time deduct the amount so paid by the Employer as aforesaid from any monies due or which may become due to the Contractor, or recover the same as a debt due from the Contractor.

#### **COMPLIANCE WITH STATUTES, REGULATIONS, ETC.**

- a) The Contractor shall give all notices and pay all fees and charges required to be given or paid by any national or State Statutes, Ordinances, Laws, Regulations or By-laws, or any local or other duly constituted authority in relation to the execution of the Works or of any Temporary Works and by the Rules and Regulations of all public bodies and companies whose property or rights are affected or may be affected in any way by the Works or any Temporary Works.
- b) The Contractor shall conform in all respects with any such Statutes, Ordinances, Laws, Regulations, By-laws or requirements of any such local or other authority which may be applicable to the Works and shall keep the Employer indemnified against all penalties and liabilities of every kind for breach of any such Statutes, Ordinances, Laws, Regulations, By-laws or requirements.

#### **27. FOSSILS, ETC.**

All fossils, coins, articles of value or antiquity and structures and other remains or things of geological or archaeological interest discovered on the Site of the Works shall as between the Employer and the Contractor be deemed to be the absolute property of the Employer and the Contractor shall take reasonable precautions to prevent his workmen or any other persons from removing or damaging any such article or thing and shall immediately upon discovery thereof and before removal acquaint the Employer of such discovery and carry out at the expense of the Employer the Engineer's orders as to the disposal of the same.

#### **28. COPYRIGHT, PATENT AND OTHER PROPRIETARY RIGHTS, AND ROYALTIES**

- a) The Contractor shall hold harmless and fully indemnify the Employer from and against all claims and proceedings for or on account of infringement of any patent rights, design trademark or name or other protected rights in respect of any Plant, equipment, machine, work or material used for or

in connection with the Works or Temporary Works and from and against all claims, demands proceedings, damages, costs, charges and expenses whatsoever in respect thereof or in relation thereto, except where such infringement results from compliance with the design or Specification provided by the Engineer.

- b) Except where otherwise specified, the Contractor shall pay all tonnage and other royalties, rent and other payments or compensation, if any, for getting stone, sand, gravel, clay or other materials required for the Works or Temporary Works.

### **29. INTERFERENCE WITH TRAFFIC AND ADJOINING PROPERTIES**

All operations necessary for the execution of the Works and for the Construction of any Temporary Works shall, so far as compliance with the requirements of the Contract permits, be carried on so as not to interfere unnecessarily or improperly with the public convenience, or the access to, use and occupation of, public or private roads and footpaths to or of properties whether in the possession of the Employer or of any other person. The Contractor shall hold harmless and indemnify the Employer in respect of all claims, demands, proceedings, damages, costs, charges and expenses whatsoever arising out of or in relation to any such matters in so far as the Contractor is responsible therefor.

### **30. EXTRAORDINARY TRAFFIC AND SPECIAL LOADS**

- a) The Contractor shall use every reasonable means to prevent any of the roads or bridges communicating with or on the routes to the Site from being damaged by any traffic of the Contractor or any of his sub-contractors and, in particular, shall select routes, choose and use vehicles and restrict and distribute loads so that any such extraordinary traffic as will inevitably arise from the moving of plant and material from and to the Site shall be limited as far as reasonably possible and so that no unnecessary damage may be occasioned to such roads and bridges.
- b) Should it be found necessary for the Contractor to move any load of Constructional Plant, machinery, preconstructed units or parts of units of work, or other thing, over part of a road or bridge, the moving whereof is likely to damage any such road or bridge unless special protection or strengthening is carried out, then the Contractor shall before moving the load on to such road or bridge, save insofar as the Contract otherwise provide, be responsible for and shall pay for the cost of strengthening any such bridge or altering or improving any such road to avoid such damage, and the Contractor shall indemnify and keep the Employer indemnified against all claims for damage to any such road or bridge caused by such movement, including such claim as may be made directly against the Employer, and shall negotiate and pay all claims arising solely out of such damage.

### **31. OPPORTUNITIES FOR OTHER CONTRACTORS**

The Contractor shall in accordance with the requirements of the Engineer afford all reasonable opportunities for carrying out their work to any other contractors employed by the Employer and their workmen and to the workmen of the Employer and of any other duly constituted authorities who may be employed in the execution on or near the Site of any work not included in the Contract or of any contract which the Employer may enter into in connection with or ancillary to the Works. If work by other contractors of the Employer as above-mentioned involves the Contractor in any



direct expenses as a result of using his Site facilities, the Employer shall consider payment to the Contractor of such sum or sums as may be recommended by the Engineer.

### **32. CONTRACTOR TO KEEP SITE CLEAN**

During the progress of the Works, the Contractor shall keep the Site reasonably free from all unnecessary obstruction and shall store or dispose of any Constructional Plant and surplus materials and clear away and remove from the Site any wreckage, rubbish or Temporary Works no longer required.

### **33. CLEARANCE OF SITE ON SUBSTANTIAL COMPLETION**

On the substantial completion of the Works, the Contractor shall clear away and remove from the Site all Constructional Plant surplus materials, rubbish and Temporary Works of every kind and leave the whole of the Site and Works clean and in a workmanlike condition to the satisfaction of the Engineer.

### **34. LABOUR**

#### **34.1 Engagement of Labour**

The Contractor shall make his own arrangements for the engagement of all labour local or otherwise.

#### **34.2 Supply of Water**

The Contractor shall provide on the Site to the satisfaction of the Engineer an adequate supply of drinking and other water for the use of the Contractor's staff and work people.

#### **34.3 Alcoholic Drinks or Drugs**

The Contractor shall comply with Government laws and regulations and orders in force as regards the import, sale, barter or disposal of alcoholic drinks or narcotics and he shall not allow or facilitate such importation, sale, gift, barter or disposal by his sub-contractors, agents or employees.

#### **34.4 Arms and Ammunition**

The restrictions specified in clause 34.3 above shall include all kinds of arms and ammunition.

#### **34.5 Holiday and Religious Customs**

The Contractor shall in all dealings with labour in his employ have due regard to all holiday, recognized festivals and religious or other customs.

#### **34.6 Epidemics**

In the event of any outbreak of illness of an epidemic nature the Contractor shall comply with and carry out such regulations, orders, and requirements as may be made by the Government or the local medical or sanitary authorities for the purpose of dealing with and overcoming the same.

### **34.7 Disorderly Conduct, etc.**

The Contractor shall at all times take all reasonable precautions to prevent any unlawful riotous or disorderly conduct by or amongst his employees and for the preservation of peace and the protection of persons and property in the neighborhood of the Works against the same.

### **34.8 Observance by Sub-Contractors**

The Contractor shall be considered responsible for the observance of the above provisions by his Sub-Contractors.

### **34.9 Legislation applicable to Labour**

The Contractor shall abide by all applicable legislation and regulation with regard to labour.

## **RETURNS OF LABOUR, PLANT, ETC.**

The Contractor shall, if required by the Engineer, deliver to the Engineer at his office, a return in detail in the form and at such intervals as the Engineer may prescribe showing the supervisory staff and the numbers of the several classes of labour from time to time employed by the Contractor on the Site and such information respecting Constructional plant as the Engineer may require.

## **MATERIALS, WORKMANSHIP AND TESTING**

### **36.1 Materials and Workmanship**

- a) All materials and workmanship shall be of the respective kinds described in the Contract and in accordance with the Engineer's instructions and shall be subjected from time to time to such tests as the Engineer may direct at the place of manufacture or fabrication, or on the Site or at all or any of such places. The Contractor shall provide such assistance, instruments, machines, labour and materials as are normally required for examining, measuring and testing any work and the quality, weight or quantity of any materials used and shall supply samples of materials before incorporation in the Works for testing as may be selected and required by the Engineer. All testing equipment and instruments provided by the Contractor shall be used only by the Engineer or by the Contractor in accordance with the instructions of the Engineer.
- b) No material not conforming with the Specifications in the Contract may be used for the Works without prior written approval of the Employer and instruction of the Engineer, provided always that if the use of such material results or may result in increasing the Contract Price, the procedure in Clause 48 shall apply.

### **36.2 Cost of Samples**

All samples shall be supplied by the Contractor at his own cost unless the supply thereof is clearly intended in the Specifications or Bill of Quantities to be at the cost of the Employer. Payment will not be made for samples which do not comply with the Specifications.

### **36.3 Cost of Tests**

The Contractor shall bear the costs of any of the following tests:

- a) Those clearly intended by or provided for in the Contract Documents.
- b) Those involving load testing or tests to ensure that the design of the whole of the Works or any part of the Works is appropriate for the purpose which it was intended to fulfill.

### **37 ACCESS TO SITE**

The Employer and the Engineer and any persons authorized by either of them shall, at all times, have access to the Works and to the Site and to all workshops and places where work is being prepared or whence materials, manufactured articles or machinery are being obtained for the Works and the Contractor shall afford every facility for and every assistance in or in obtaining the right to such access.

### **38 EXAMINATION OF WORK BEFORE COVERING UP**

No work shall be covered up or put out of view without the approval of the Engineer and the Contractor shall afford full opportunity for the Engineer to examine and measure any work which is about to be covered up or put out of view and to examine foundations before permanent work is placed thereon. The Contractor shall give due notice to the Engineer whenever any such work or foundations is or are ready or about to be ready for examination and the Engineer shall without unreasonable delay unless he considers it unnecessary and advises the Contractor accordingly attend for the purpose of examining and measuring such work or of examining such foundations.

### **39 REMOVAL OF IMPROPER WORK AND MATERIALS**

#### **39.1 Engineer's power to order removal**

The Engineer shall during the progress of the Works have power to order in writing from time to time, and the Contractor shall execute at his cost and expense, the following operations:

- a) The removal from the Site within such time or times as may be specified in the order of any materials which in the opinion of the Engineer are not in accordance with the Contract;
- b) The substitution of proper and suitable materials; and
- c) The removal and proper re-execution (notwithstanding any previous test thereof or interim payment therefore) of any work which in respect of materials or workmanship is not in the opinion of the Engineer in accordance with the Contract.

#### **39.2 Default of Contractor in carrying out Engineer's Instructions**

In case of default on the part of the Contractor in carrying out an instruction of the Engineer, the Employer shall be entitled to employ and pay other persons to carry out the same and all expenses consequent thereon or incidental thereto shall be borne by the Contractor and shall be recoverable from him by the Employer and may be deducted by the Employer from any monies due or which may become due to the Contractor.

#### **40 SUSPENSION OF WORK**

The Contractor shall on the written order of the Engineer suspend the progress of the Works or any part thereof for such time or times and in such manner as the Engineer may consider necessary and shall, during such suspension, properly protect and secure the Works so far as it is necessary in the opinion of the Engineer. The Employer should be notified and his written approval should be sought for any suspension of work in excess of three (3) days.

#### **41 POSSESSION OF SITE**

##### **41.1 Access to Site**

The Employer shall with the Engineer's written order to commence the Works, give to the Contractor possession of so much of the Site as may be required to enable the Contractor to commence and proceed with the construction of the Works in accordance with the Programme referred to in Clause 13 hereof and otherwise in accordance with such reasonable proposals of the Contractor as he shall make to the Engineer by notice in writing, and shall from time to time as the Works proceed give to the Contractor possession of such further portions of the Site as may be required to enable the Contractor to proceed with the construction of the Works with due dispatch in accordance with the said Programme or proposals, as the case may be.

##### **41.2 Wayleaves, etc.**

The Contractor shall bear all expenses and charges for special temporary wayleaves required by him in connection with access to the Site. The Contractor shall also provide at his own cost any additional accommodation outside the Site required by him for the purpose of the Works.

##### **41.3 Limits of the Site**

Except as defined below, the limits of the Site shall be as defined in the Contract. Should the Contractor require land beyond the Site, he shall provide it entirely at his own expense and before taking possession shall supply the Engineer with a copy of the necessary permits. Access to the Site is available where the Site adjoins a public road but it is not provided unless shown on the Drawings. When necessary for the safety and convenience of workmen, public or livestock or for the protection of the Works, the Contractor shall, at his own expense, provide adequate temporary fencing to the whole or part of the Site. The Contractor shall not disturb, damage or pull down any hedge, tree or building within the Site without the written consent of the Engineer.

#### **42 TIME FOR COMPLETION**

- a) Subject to any requirement in the Contract as to completion of any section of the Works before completion of the whole, the whole of the Works shall be completed, in accordance with the provisions of Clause 46 and 47 hereof, within the time stated in the Contract.
- b) The completion time includes weekly rest days, official holidays, and days of inclement weather.

#### **43 EXTENSION OF TIME FOR COMPLETION**

If, subject to the provisions of the Contract, the Engineer orders alterations or additions in the Works in accordance with Clause 48 hereof, or if circumstances constituting force majeure as defined in the Contract have occurred, the Contractor shall be entitled to apply for an extension of the time for completion of the Works specified in the Contract. The Employer shall, upon such application, determine the period of any such extension of time; provided that in the case of alterations or additions in the Works, the application for such an extension must be made before the alterations or additions in the Works are undertaken by the Contractor.

#### **44 RATE OF PROGRESS**

The whole of the materials, plant and labour to be provided by the Contractor and the mode, manner and speed of execution and completion of the Works are to be of a kind and conducted in a manner to the satisfaction of the Engineer. Should the rate of progress of the Works or any part thereof be at any time in the opinion of the Engineer too slow to ensure the completion of the Works by the prescribed time or extended time for completion, the Engineer shall so notify the Contractor in writing and the Contractor shall thereupon take such steps as the Contractor may think necessary and the Engineer may approve to expedite progress so as to complete the Works by the prescribed time or extended time for completion. If the work is not being carried on by day and by night and the Contractor shall request permission to work by night as well as by day, then, if the Engineer shall grant such permission, the Contractor shall not be entitled to any additional payment. All work at night shall be carried out without unreasonable noise and disturbance. The contractor shall indemnify the Employer from and against any claims or liability for damages on account of noise or other disturbance created while or in carrying out the work and from and against all claims, demands, proceedings, costs and expenses whatsoever in regard or in relation to such noise or other disturbance. The Contractor shall submit in triplicate to the Engineer at the end of each month signed copies of explanatory Drawings or any other material showing the progress of the Works.

#### **45 LIQUIDATED DAMAGES FOR DELAY**

- a) If the Contractor shall fail to complete the Works within the time for completion prescribed in the Contract, or any extended time for completion in accordance with the Contract, then the Contractor shall pay to the Employer the sum specified in the Contract as liquidated damages, for the delay between the time prescribed in the Contract or the extended time for completion, as the case may be, and the date of substantial completion of the Works as stated in the Certificate of Substantial Completion, subject to the applicable limit stated in the Contract. The said sum shall be payable by the sole fact of the delay without the need for any previous notice or any legal proceedings, or proof of damage, which shall in all cases be considered as ascertained. The Employer may, without prejudice to any other method of recovery, deduct the amount of such liquidated damages from any monies in its hands due or which may become due to the Contractor. The payment or deduction of such damages shall not relieve the Contractor from his obligation to complete the Works or from any other of his obligations and liabilities under the Contract.
- b) If, before the time for completion of the whole of the Works or of a Section of the Works, a Certificate of Substantial Completion has been issued for any part or Section of the Works, the liquidated damages for delay in completion of the remainder of the Works or of that Section may, for any period of delay after the date stated in such Certificate of Substantial Completion, and in the absence of alternative provisions in the Contract, be reduced in the proportion which the value of the part or Section so certified bears to the total value of the whole of the Works or Section, as

applicable. The provisions of this Sub-Clause shall only apply to the rate of liquidated damages and shall not affect the limit thereof.

## **46 CERTIFICATE OF SUBSTANTIAL COMPLETION**

### **46.1 Substantial Completion of the Works**

When the whole of the Works have been substantially completed and have satisfactorily passed any test on completion prescribed by the Contract, the Contractor may give a notice to that effect to the Engineer accompanied by an undertaking to finish any outstanding work during the Defects Liability Period. Such notice and undertaking shall be in writing and shall be deemed to be a request by the Contractor, for the Engineer to issue a Certificate of Substantial Completion in respect of the Works. The Engineer shall, within twenty-one (21) days of the date of delivery of such notice either issue to the Contractor, with a copy to the Employer, a Certificate of Substantial Completion stating the date on which, in his opinion, the Works were substantially completed in accordance with the Contract or give instructions in writing to the Contractor specifying all the work which, in the Engineer's opinion, requires to be done by the Contractor before the issuance of such Certificate. The Engineer shall also notify the Contractor of any defects in the Works affecting substantial completion that may appear after such instructions and before completion of the work specified therein. The Contractor shall be entitled to receive such Certificate of Substantial Completion within twenty-one (21) days of completion, to the satisfaction of the Engineer, of the work so specified and making good any defect so notified. Upon issuance of the Certificate of Substantial Completion of the Works, the Contractor shall be deemed to have undertaken to complete with due expedition any outstanding work during the Defects Liability Period.

### **46.2 Substantial Completion of Sections or Parts of the Works**

In accordance with the procedure in Sub-Clause (1) of this Clause and on the same conditions as provided therein, the Contractor may request the Engineer to issue, and the Engineer may issue, a Certificate of Substantial Completion in respect of any Section or part of the Works which has been substantially completed and has satisfactorily passed any tests on completion prescribed by the Contract, if:

- a) a separate time for completion is provided in the Contract in respect of such Section or part of the Works;
- b) such Section or part of the Works has been completed to the satisfaction of the Engineer and is required by the Employer for his occupation or use.

Upon the issuance of such Certificate, the Contractor shall be deemed to have undertaken to complete any outstanding work during the Defects Liability Period.

## **47 DEFECTS LIABILITY**

### **47.1 Defects Liability Period**

The expression "Defects Liability Period" shall mean the period of twelve (12) months, calculated from the date of completion of the Works stated in the Certificate of Substantial Completion issued by the Engineer or, in respect of any Section or part of the Works for which a separate Certificate of

Substantial Completion has been issued, from the date of completion of that Section or part as stated in the relevant Certificate. The expression "the Works" shall, in respect of the Defects Liability Period, be construed accordingly.

#### **47.2 Completion of Outstanding Work and Remedying of Defects**

During the Defects Liability Period, the Contractor shall finish the work, if any, outstanding at the date of the Certificate of Substantial Completion, and shall execute all such work of repair, amendment, reconstruction, rectification and making good defects, imperfections, shrinkages or other faults as may be required of the Contractor in writing by the Engineer during the Defects Liability Period and within fourteen (14) days after its expiration, as a result of an inspection made by or on behalf of the Engineer prior to expiration of the Defects Liability Period.

#### **47.3 Cost of Execution of Work of Repair, etc.**

All such outstanding work shall be carried out by the Contractor at his own expense if the necessity thereof shall, in the opinion of the Engineer, be due to the use of material or workmanship not in accordance with the Contract, or to neglect or failure on the part of the Contractor to comply with any obligation expressed or implied, on the Contractor's part under the Contract.

#### **47.4 Remedy on Contractor's Failure to Carry Out Work Required**

If the Contractor shall fail to do any such work outstanding on the Works, the Employer shall be entitled to employ and pay other persons to carry out the same, and all expenses consequent thereon or incidental thereto shall be recoverable from the Contractor by the Employer, and may be deducted by the Employer from any monies due or which may become due to the Contractor.

#### **47.5 Certificate of Final Completion**

Upon satisfactory completion of the work outstanding on the Works, the Engineer shall within twenty eight (28) days of the expiration of the Defects Liability period issue a Certificate of Final Completion to the Contractor. The Contract shall be deemed to be completed upon issuance of such Certificate, provided that the provisions of the Contract which remain unperformed and the Settlement of Disputes provision in the Contract shall remain in force for as long as is necessary to dispose of any outstanding matters or issues between the Parties.

### **48 ALTERATIONS, ADDITIONS AND OMISSIONS**

#### **1 Variations**

The Engineer may within his powers introduce any variations to the form, type or quality of the Works or any part thereof which he considers necessary and for that purpose or if for any other reasons it shall, in his opinion be desirable, he shall have power to order the Contractor to do and the Contractor shall do any of the following:

- (a) increase or decrease the quantity of any work under the Contract;
- (b) omit any such work;

- (c) change the character or quality or kind of any such work;
- (d) change the levels, lines, positions and dimensions of any part of the Works;
- (e) execute additional work of any kind necessary for the completion of the Works, and no such variation shall in any way vitiate or invalidate the Contract.

## **2 Variations Increasing Cost of Contract or altering the Works.**

The Engineer shall, however, obtain the written approval of the Employer before giving any order for any variations which may result in an increase of the Contract Price or in an essential alteration of the quantity, quality or character of the Works.

## **3 Orders for Variations to be in Writing**

No variations shall be made by the Contractor without an order in writing from the Engineer. Variations requiring the written approval of the Employer under paragraph (2) of this Clause shall be made by the Contractor only upon written order from the Engineer accompanied by a copy of the Employer's approval. Provided that, subject to the provisions of the Contract, no order in writing shall be required for any increase or decrease in the quantity of any work where such increase or decrease is not the result of an order given under this Clause but is the result of the quantities exceeding or being less than those stated in the Bill of Quantities.

## **4 Valuation of Variations**

The Engineer shall estimate to the Employer the amount to be added or deducted from the Contract Price in respect of any variation, addition or omission. In the case of any variation, addition or omission which may result in an increase of the Contract Price, the Engineer shall communicate such estimate to the Employer together with his request for the Employer's written approval of such variation, addition or omission. The value of any variation, addition or omission shall be calculated on the basis of the unit prices contained in the Bill of Quantities.

## **49 PLANT, TEMPORARY WORKS AND MATERIALS**

### **1 Plant, etc., Exclusive Use for the Works**

All Constructional Plant, Temporary Works and Materials provided by the Contractor shall, when brought on the Site, be deemed to be exclusively intended for the construction and completion of the Works and the Contractor shall not remove the same or any part thereof (save for the purpose of moving it from one part of the Site to another) without the consent in writing of the Engineer which shall not be unreasonably withheld.

### **2 Removal of Plant, etc.**

Upon completion of the Works the Contractor shall remove from the Site all the said Constructional Plant and Temporary Works remaining thereon and any unused materials provided by the Contractor.



### **3 Employer not liable for Damage to Plant**

The Employer shall not be at any time liable for the loss of any of the said Constructional plant, Temporary Works or Materials save if such loss results from the act or neglect of the Employer, its employees or agents.

### **4 Ownership of paid material and work**

All material and work covered by payments made by the Employer to the Contractor shall thereupon become the sole property of the Employer, but this provision shall not be construed as relieving the Contractor from the sole responsibility for all material and work upon which payments have been made or the restoration of any damaged work or as waiving the right of the Employer to require the fulfillment of all of the terms of the Contract.

### **5 Equipment and supplies furnished by Employer**

Title to any equipment and supplies which may be furnished by the Employer shall rest with the Employer and any such equipment and supplies shall be returned to the Employer at the conclusion of the Contract or when no longer needed by the Contractor. Such equipment when returned to the Employer, shall be in the same condition as when delivered to the Contractor, subject to normal wear and tear.

### **50 APPROVAL OF MATERIALS ETC., NOT IMPLIED**

The operation of Clause 49 hereof shall not be deemed to imply any approval by the Engineer of the materials or other matters referred to therein nor shall it prevent the rejection of any such materials at any time by the Engineer.

### **51 MEASUREMENT OF WORKS**

The Engineer shall, when he requires any part or parts of the Works to be measured, give notice to the Contractor or the Contractor's authorized agent or representative who shall forthwith attend or send a qualified agent to assist the Engineer in making such measurement and shall furnish all particulars required by either of them. Should the Contractor not attend or neglect or omit to send such agent, then the measurement made by the Engineer or approved by him shall be taken to be the correct measurement of the work. The purpose of measuring is to ascertain the volume of work executed by the Contractor and therefore determine the amount of the monthly payments.

### **52 LIABILITY OF THE PARTIES**

- 1** The Works shall not be considered as completed until a Certificate of Final Completion shall have been signed by the Engineer and delivered to the Employer stating that the Works have been completed and that the Contractor has fulfilled all his obligations under Clause 47 to his satisfaction.

2 The Employer shall not be liable to the Contractor for any matter arising out of or in connection with the Contract or the execution of the Works unless the Contractor shall have made a claim in writing in respect thereof before the giving of the Certificate of Final Completion and in accordance with the Contract.

### 3 Unfulfilled Obligations

Notwithstanding the issue of the Certificate of Final Completion, the Contractor shall remain liable for the fulfillment of any obligation incurred under the provisions of the Contract prior to the issuance of the Certificate of Final Completion and which remains unperformed at the time such Certificate is issued. For the purpose of determining the nature and extent of any such obligation the Contract shall be deemed to remain in force between the parties hereto.

### 4 Contractor Responsible

Notwithstanding any other provisions in the Contract documents, the Contractor shall be totally responsible for and shall bear any and all risks of loss or damage to or failure of the Works or any part thereof for a period of ten years after issuance of the Certificate of Final Completion, provided always that such risks, damage or failure result from acts, defaults and negligence of the Contractor, his agents, employees or workmen and such contractors.

## 53 AUTHORITIES

1 The Employer shall have the right to enter upon the Site and expel the Contractor therefrom without thereby voiding the Contract or releasing the Contractor from any of his obligations or liabilities under the Contract or affecting the rights and powers conferred on the Employer and the Engineer by the Contract in any of the following cases:

- (a) If the Contractor is declared bankrupt or claims bankruptcy or court protection against his creditors or if the Contractor is a company or member of a company which was dissolved by legal action;
- (b) If the Contractor makes arrangements with his creditors or agrees to carry out the Contract under an inspection committee of his creditors;
- (c) If the Contractor withdraws from the Works or assigns the Contract to others in whole or in part without the Employer's prior written approval;
- (d) If the Contractor fails to commence the Works or shows insufficient progress to the extent which in the opinion of the Engineer will not enable him to meet the target completion date of the Works;
- (e) If the Contractor suspends the progress of the Works without due cause for fifteen (15) days after receiving from the Engineer written notice to proceed;
- (f) If the Contractor fails to comply with any of the Contract conditions or fails to fulfill his obligations and does not remedy the cause of his failure within fifteen (15) days after being notified to do so in writing;

- (g) If the Contractor is not executing the work in accordance with standards of workmanship specified in the Contract;
- (h) If the Contractor gives or promises to give a present or loan or reward to any employee of the Employer or of the Engineer.

Then the Employer may himself complete the Works or may employ any other contractor to complete the Works and the Employer or such other contractor may use for such completion so much of Constructional Plant, Temporary Works and Materials, which have been deemed to be reserved exclusively for the construction and completion of the Works under the provision of the Contract as he or they may think proper and the Employer may at any time sell any of the said Constructional Plant, Temporary Works and unused materials and apply the proceeds of sale in or towards the satisfaction of any sums due or which may become due to him from the Contractor under the Contract.

## 2 Evaluation after Re-entry

The Engineer shall as soon as may be practicable after any such entry and expulsion by the Employer notify the Contractor to attend the necessary evaluation of the Works. In the event that for any reason the Contractor does not attend such evaluation the Engineer shall undertake the said evaluation in the absence of the Contractor and shall issue a certificate stating the sum, if any, due to the Contractor for work done in accordance with the Contract up to the time of entry and expulsion by the Employer which has been reasonably accumulated to the Contractor in respect of the Works he has executed in such case in accordance with the Contract. The Engineer shall indicate the value of the materials whether unused or partially used and the value of construction equipment and any part of the Temporary Works.

## 3 Payment After Re-entry

If the Employer shall enter and expel the Contractor under this Clause he shall not be liable to pay the Contractor any money on account of the Contract until the expiration of the Defects Liability Period, and thereafter until the costs of completion and making good any defects of the Works, damages for delay in completion (if any), and all other expenses incurred by the Employer have been ascertained and their amount certified by the Engineer. The Contractor shall then be entitled to receive only such sum or sums (if any) as the Engineer may certify would have been due to him upon due completion by him after deducting the said amount. But if such amount shall exceed the sum which would have been payable to the Contractor on due completion by him, then the Contractor shall upon demand pay to the Employer the amount of such excess. The Employer in such case may recover this amount from any money due to the Contractor from the Employer without the need to resort to legal procedures.

## 54 URGENT REPAIRS

If by reason of any accident or failure or other event occurring to, in or in connection with the Works or any part thereof either during the execution of the Works or during the Defects Liability Period any remedial or other work or repair shall in the opinion of the Engineer be urgently necessary for security and the Contractor is unable or unwilling at once to do such work or repair, the Employer may by his own or other workmen do such work or repair as the Engineer may consider necessary. If

the work or repair so done by the Employer is work which in the opinion of the Engineer the Contractor was liable to do at his own expense under the Contract, all costs and charges properly incurred by the Employer in so doing shall on demand be paid by the Contractor to the Employer or may be deducted by the Employer from any monies due or which may become due to the Contractor provided always that the Engineer shall as soon after the occurrence of any such emergency as may be reasonably practicable notify the Contractor thereof in writing.

## **55 INCREASE AND DECREASE OF COSTS**

Except if otherwise provided by the Contract, no adjustment of the Contract Price shall be made in respect of fluctuations of market, prices of labour, materials, plant or equipment, neither due to fluctuation in interest rates nor devaluation or any other matters affecting the Works.

## **56 TAXATION**

The Contractor shall be responsible for the payment of all charges and taxes in respect of income including value added tax, all in accordance with and subject to the provisions of the income tax laws and regulations in force and all amendments thereto. It is the Contractor's responsibility to make all the necessary inquiries in this respect and he shall be deemed to have satisfied himself regarding the application of all relevant tax laws.

## **57 BLASTING**

The Contractor shall not use any explosives without the written permission of the Engineer who shall require that the Contractor has complied in full with the regulations in force regarding the use of explosives. However, the Contractor, before applying to obtain these explosives, has to provide well arranged storage facilities. The Engineer's approval or refusal to permit the use of explosives shall not constitute ground for claims by the Contractor.

## **58 MACHINERY**

The Contractor shall be responsible for coordinating the manufacture, delivery, erection and commissioning of plant machinery and equipment which are to form a part of the Works. He shall place all necessary orders as soon as possible after the signing of the Contract. These orders and their acceptance shall be produced to the Engineer on request. The Contractor shall also be responsible for ensuring that all sub-contractors adhere to such programs as are agreed and are needed to ensure completion of the Works within the period for completion. Should any sub-contracted works be delayed, the Contractor shall initiate the necessary action to speed up such completion. This shall not prejudice the Employer's right to exercise his remedies for delay in accordance with the Contract.

## **59 TEMPORARY WORKS AND REINSTATEMENT**

The Contractor shall provide and maintain all temporary roads and tracks necessary for movement of plant and materials and clear same away at completion and make good all works damaged or disturbed. The Contractor shall submit drawings and full particulars of all Temporary Works to the Engineer before commencing same. The Engineer may require modifications to be made if he considers them to be insufficient and the Contractor shall give effect to such modifications but shall not be relieved of his responsibilities. The Contractor shall provide and maintain weather-proof sheds for storage of material pertinent to the Works both for his own use and for the use of the Employer and clear same away at the completion of the Works. The Contractor shall divert as required, at his own cost and subject to the approval of the Engineer, all public utilities encountered during the progress of the Works, except those specially indicated on the drawings as being included in the Contract. Where diversions of services are not required in connection with the Works, the Contractor shall uphold, maintain and keep the same in working order in existing locations. The Contractor shall make good, at his own expense, all damage to telephone, telegraph and electric cable or wires, sewers, water or other pipes and other services, except where the Public Authority or Private Party owning or responsible for the same elects to make good the damage. The costs incurred in so doing shall be paid by the Contractor to the Public Authority or Private Party on demand.

## **60 PHOTOGRAPHS AND ADVERTISING**

The Contractor shall not publish any photographs of the Works or allow the Works to be used in any form of advertising whatsoever without the prior approval in writing from the Employer.

## **61 PREVENTION OF CORRUPTION**

The Employer shall be entitled to cancel the Contract and to recover from the Contractor the amount of any loss resulting from such cancellation, if the Contractor has offered or given any person any gift or consideration of any kind as an inducement or reward for doing or intending to do any action in relation to the obtaining or the execution of the Contract or any other contract with the Employer or for showing or intending to show favour or disfavour to any person in relation to the Contract or any other contract with the Employer, if the like acts shall have been done by any persons employed by him or acting on his behalf whether with or without the knowledge of the Contractor in relation to this or any other Contract with the Employer.

## **62 DATE FALLING ON HOLIDAY**

Where under the terms of the Contract any act is to be done or any period is to expire upon a certain day and that day or that period fall on a day of rest or recognized holiday, the Contract shall have effect as if the act were to be done or the period to expire upon the working day following such day.

## **63 NOTICES**

- 1** Unless otherwise expressly specified, any notice, consent, approval, certificate or determination by any person for which provision is made in the Contract Documents shall be in writing. Any such

- notice, consent, approval, certificate or determination to be given or made by the Employer, the Contractor or the Engineer shall not be
- 2 unreasonably withheld or delayed.
  - 3 Any notice, certificate or instruction to be given to the Contractor by the Engineer or the Employer under the terms of the Contract shall be sent by post, cable, telex or facsimile at the Contractor's principal place of business specified in the Contract or such other address as the Contractor shall nominate in writing for that purpose, or by
  - 4 delivering the same at the said address against an authorized signature certifying the receipt.
  - 5 Any notice to be given to the Employer under the terms of the Contract shall be sent by post, cable, telex or facsimile at the Employer's address specified in the Contract, or by delivering the same at the said address against an authorized signature certifying the receipt.
  - 6 Any notice to be given to the Engineer under the terms of this Contract shall be sent by post, cable, telex or facsimile at the Engineer's address specified in the Contract, or by delivering the same at the said address against an authorized signature certifying the receipt.

#### 64 LANGUAGE, WEIGHTS AND MEASURES

Except as may be otherwise specified in the Contract, English shall be used by the Contractor in all written communications to the Employer or the Engineer with respect to the services to be rendered and with respect to all documents procured or prepared by the Contractor pertaining to the Works. The metric system of weights and measures shall be used in all instances.

#### 65 RECORDS, ACCOUNTS, INFORMATION AND AUDIT

The Contractor shall maintain accurate and systematic records and accounts in respect of the work performed under this Contract.

The Contractor shall furnish, compile or make available at all times to the UNDP any records or information, oral or written, which the UNDP may reasonably request in respect of the Works or the Contractor's performance thereof.

The Contractor shall allow the UNDP or its authorized agents to inspect and audit such records or information upon reasonable notice.

#### 66 FORCE MAJEURE

Force majeure as used herein means Acts of God, war (whether declared or not), invasion, revolution, insurrection or other acts or events of a similar nature or force.

In the event of and as soon as possible after the occurrence of any cause constituting force majeure, the Contractor shall give notice and full particulars in writing to the UNDP and to the Engineer of such force majeure if the Contractor is thereby rendered unable, wholly or in part, to perform its obligations and meet its responsibilities under this Contract. Subject to acceptance by the UNDP of

the existence of such force majeure, which acceptance shall not be unreasonably withheld, the following provisions shall apply:

- (a) The obligations and responsibilities of the Contractor under this Contract shall be suspended to the extent of his inability to perform them and for as long as such inability continues. During such suspension and in respect of work suspended, the Contractor shall be reimbursed by the UNDP substantiated costs of maintenance of the Contractor's equipment and of per diem of the Contractor's permanent personnel rendered idle by such suspension;
- (b) The Contractor shall within fifteen (15) days of the notice to the UNDP of the occurrence of the force majeure submit a statement to the UNDP of estimated costs referred to in sub-paragraph (a) above during the period of suspension followed by a complete statement of actual expenditures within thirty (30) days after the end of the
- (c) suspension;
- (d) The term of this Contract shall be extended for a period equal to the period of suspension taking however into account any special condition which may cause the additional time for completion of the Works to be different from the period of suspension;
- (e) If the Contractor is rendered permanently unable, wholly or in part, by reason of force majeure, to perform his obligations and meet his responsibilities under the Contract, the UNDP shall have the right to terminate the Contract on the same terms and conditions as provided for in Clause 68 of these General Conditions, except that the period of notice shall be seven (7) days instead of fourteen (14) days, and
- (f) For the purpose of the preceding sub-paragraph, the UNDP may consider the Contractor permanently unable to perform in case of any suspension period of more than ninety (90) days.

## **67 SUSPENSION BY THE UNDP**

The UNDP may by written notice to the Contractor suspend for a specified period, in whole or in part, payments to the Contractor and/or the Contractor's obligation to continue to perform the Works under this Contract, if in the UNDP's sole discretion:

- (a) any conditions arise which interfere, or threaten to interfere with the successful execution of the Works or the accomplishment of the purpose thereof, or
- (b) the Contractor shall have failed, in whole or in part, to perform any of the terms and conditions of this Contract.

After suspension under sub-paragraph (a) above, the Contractor shall be entitled to reimbursement by the UNDP of such costs as shall have been duly incurred in accordance with this Contract prior to the commencement of the period of such suspension.

The term of this Contract may be extended by the UNDP for a period equal to any period of suspension, taking into account any special conditions which may cause the additional time for completion of the Works to be different from the period of suspension.

## 68 TERMINATION BY THE UNDP

The UNDP may, notwithstanding any suspension under Clause 67 above, terminate this Contract for cause or convenience in the interest of the UNDP upon not less than fourteen (14) days written notice to the Contractor.

Upon termination of this Contract:

- (a) The Contractor shall take immediate steps to terminate his performance of the Contract in a prompt and orderly manner and to reduce losses and to keep further expenditures to a minimum, and
- (b) The Contractor shall be entitled (unless such termination has been occasioned by the Contractor's breach of this Contract), to be paid for the part of the Works satisfactorily completed and for the materials and equipment properly delivered to the Site as of the date of termination for incorporation to the Works, plus substantiated costs resulting from commitments entered into prior to the date of termination as well as any reasonable substantiated direct costs incurred by the Contractor as a result of the termination, but shall not be entitled to receive any other or further payment or damages.

## 69 TERMINATION BY THE CONTRACTOR

In the case of any alleged breach by the UNDP of the Contract or in any other situation which the Contractor reasonably considers to entitle him to terminate his performance of the Contract, the Contractor shall promptly give written notice to the UNDP detailing the nature and the circumstances of the breach or other situation. Upon acknowledgement in writing by the UNDP of the existence of such breach and the UNDP's inability to remedy it, or upon failure of the UNDP to respond to such notice within twenty (20) days of receipt thereof, the Contractor shall be entitled to terminate this Contract by giving 30 days written notice thereof. In the event of disagreement between the Parties as to the existence of such breach or other situation referred to above, the matter shall be resolved in accordance with Clause 71 of these General Conditions.

Upon termination of this Contract under this Clause the provisions of sub-paragraph (b) of Clause 68 hereof shall apply.

## 70 RIGHTS AND REMEDIES OF THE UNDP

Nothing in or relating to this Contract shall be deemed to prejudice or constitute a waiver of any other rights or remedies of the UNDP.

The UNDP shall not be liable for any consequences of, or claim based upon, any act or omission on the part of the Government.

## 71 SETTLEMENT OF DISPUTES



In the case of any claim, controversy or dispute arising out of, or in connection with this Contract or any breach thereof, the following procedure for resolution of such claim, controversy or dispute shall apply.

**1 Notification**

The aggrieved party shall immediately notify the other party in writing of the nature of the alleged claim, controversy or dispute, not later than seven (7) days from awareness of the existence thereof.

**2 Consultation**

On receipt of the notification provided above, the representatives of the Parties shall start consultations with a view to reaching an amicable resolution of the claim, controversy or dispute without causing interruption of the Works.

**3 Conciliation**

Where the representatives of the Parties are unable to reach such an amicable settlement, either party may request the submission of the matter to conciliation in accordance with the UNCITRAL Rules of Conciliation then obtaining.

**4 Arbitration**

Any claim, controversy or dispute which is not settled as provided under clauses 71.1 through 3 above shall be referred to arbitration in accordance with the UNCITRAL Arbitration Rules then obtaining. The Parties shall be bound by the arbitration award rendered in accordance with such arbitration as the final adjudication of any such controversy or claim.

**72 PRIVILEGES AND IMMUNITIES**

Nothing in or relating to this Contract shall be deemed a waiver of any of the privileges and immunities of the United Nations of which the UNDP is an integral part.
